

**SOUTH FIRE DISTRICT
Of the City of Middletown
BUILDING COMMITTEE MEETING
Monday, June 14, 2021
5:30 p.m.**

AGENDA

- 1. CALL TO ORDER**
- 2. OPEN PUBLIC SESSION**
- 3. CLOSE PUBLIC SESSION**
- 4. APPROVAL OF MINUTES**
 - a.** Building Committee Meeting of May 10, 2021.
- 5. OLD BUSINESS**
 - a.** Project update – Landmark Architects, P.C.
- 6. NEW BUSINESS**
 - a.** Project finances
 - b.** Approval of bid documents, contracts, change orders or invoices required for the project.
 - c.** Dedication Plaque
 - d.** Discussion for Dedication Date
- 7. ADJOURNMENT**

The firehouse is currently closed to the public.
Members of the public can join the meeting via Zoom.

Visit <https://us02web.zoom.us/j/86127969312>
or Dial In - 646-558-8656 to join remotely.
Meeting I.D. 86127969312

**SOUTH FIRE DISTRICT
Of the City of Middletown
BUILDING COMMITTEE MEETING
Monday, May 10, 2021
5:30 p.m.**

MINUTES

Present: Chairman Thazhampallath, Joseph Bibisi, Edward Creem, Gene Nocera, Philip Pessina, Guy Russo, Phil Russo, Chief Michael Howley, Paul Pizzo, and Paul Morin, Board of Fire Commissioners Chairwoman Deborah Kleckowski, and members of the fire department.

Absent: Nancy Hunter

1. CALL TO ORDER Chairman Thazhampallath called the meeting to order at 5:41 p.m.
2. OPEN PUBLIC SESSION Chairman Thazhampallath opened the Public Session at 5:32 p.m. *Deborah Kleckowski, SFD Board of Fire Commissioners Chairwoman*
She would like to encourage the Committee to focus on coming to a resolution with the Local 3918 regarding the addition of solartubes in the lounge and the removal of the wall between the existing Fire Chief's office and the lounge.
3. CLOSE PUBLIC SESSION Chairman Thazhampallath closed the Public Session at 5:44 p.m.
4. APPROVAL OF MINUTES
 - a. Building Committee Meeting of April 12, 2021.
MOTION to approve the minutes of April 12, 2021 by E. Creem/G. Russo. Philip Pessina abstained. Motion passed.
5. OLD BUSINESS
 - a. Project update – Landmark Architects, P.C.
6. NEW BUSINESS
 - a. Project finances
 - b. Approval of bid documents, contracts, change orders or invoices required for the project.

Paul Morin reviewed the payment application with the committee, as well, as the phases of the project and the items included in each phase. He informed the committee Phase 1 will be completed on Tuesday, May 11th and the district will

have temporary use of the new space. He also prepared a punch list for the contractor.

MOTION to approve invoice number four (4) in the amount of \$245,553.00 for payment to Enterprise Builders, Inc. by G. Pessina/E. Creem. Unanimously approved.

Paul Morin reviewed the potential change orders with the committee.

- PCO #4– Addition of Solartube Daylighting in the lounge.
MOTION to approve up to two (2) Solartubes in the lounge at a cost of \$5,239 each pending advice from the Board of Fire Commissioners by G. Russo/E. Creem. Unanimously approved.
- PCO #6 – Fan Coil Units (AC) for front offices.
MOTION to approve by G. Russo/P. Pessina. Unanimously approved.
- PCO #10 – Demolition of existing partition in lounge.
MOTION to reject due to the contractor's price too high. Refer to the South Fire District Board of Fire Commissioners by G. Russo/E/ Creem. Unanimously approved.

Generator confirmed for 100kw load. Higgins Electric to install outside boiler room on a pad for a quote of \$65,000. There will be a workshop at the City of Middletown via WebEx to discuss how regulations apply to the use of the American Recovery Act money. Discussion of a letter to City officials for possible appropriation of funds for the generator or a LoCIP application.

- PCO #13 – Provide working platform in existing electrical room pending code modification.
MOTION to approve by G. Russo/E. Creem. Unanimously approved.
- NEW PCO #16 – Eagle Environmental, Inc. for asbestos abatement re-occupancy clearance by PCM Analyses.
First payment: \$ 550.00
Second payment projection: \$1,260.00
Total: \$1,810.00

MOTION to approve by G. Russo/E. Creem. Unanimously approved.

Chairman Thazhampallath recognized Chief Howley for his work on the project, as this would be his last meeting with the Committee as the Fire Chief.

7. ADJOURNMENT

MOTION to adjourn by E. Creem/G. Russo. Unanimously approved.

The meeting adjourned at 6:39 p.m.

Submitted by,



Kathleen M. Kiley
Building Committee Secretary

APPLICATION AND CERTIFICATE FOR PAYMENT

DOCUMENT SUMMARY SHEET

TO OWNER/CLIENT:
City of Middletown
245 Dekoven Drive
Middletown, Connecticut 06457

PROJECT:
South Fire District Renovations and Addition
445 Randolph Road
Middletown, Connecticut 06457

FROM CONTRACTOR:
Enterprise Builders, Inc.
46 Shepard Drive
Newington, Connecticut 06111

VIA ARCHITECT/ENGINEER:
Paul Morin (Landmark Architects, P.C.)
100 Riverview Center, Suite 204
Middletown, Connecticut 06457

CONTRACT FOR: South Fire District Prime Contract
CONTRACTOR'S APPLICATION FOR PAYMENT

Application is made for payment, as shown below, in connection with the Contract. Continuation Sheet is attached.

1. Original Contract Sum		\$ 1,113,191.00
2. Net change by change orders		(\$2,419.00)
3. Contract sum to date (line 1 ± 2)		\$ 1,110,772.00
4. Total completed and stored to date (Column G on detail sheet)		\$ 903,320.00
5. Retainage:		
a. <u>5.00%</u> of completed work:	\$ 45,166.00	
b. <u>0.00%</u> of stored material:	\$ 0.00	
Total retainage (Line 5a + 5b or total in column I of detail sheet)		\$ 45,166.00
6. Total earned less retainage (Line 4 less Line 5 Total)		\$ 858,154.00
7. Less previous certificates for payment (Line 6 from prior certificate)		\$ 626,338.00
8. Current payment due:		\$ 231,816.00
9. Balance to finish, including retainage (Line 3 less Line 6)		\$ 252,618.00

CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous months by Owner/Client:	\$ 0.00	\$ 0.00
Total approved this Month:	\$ 4,018.00	(\$6,437.00)
Totals:	\$ 4,018.00	(\$6,437.00)
Net change by change orders:		(\$2,419.00)

APPLICATION NO: 5
INVOICE NO: 538-05
PERIOD: 05/01/21 - 05/31/21
PROJECT NO: 538
CONTRACT DATE: 01/07/2021

DISTRIBUTION TO:

The undersigned certifies that to the best of the Contractor's knowledge, information and belief, the Work covered by this Application for Payment has been completed in accordance with the Contract documents, that all amounts have been paid by the Contractor for Work which previous Certificates for payment were issued and payments received from the Owner/Client, and that current payments shown herein is now due.

CONTRACTOR: Enterprise Builders, Inc.

By: _____

Date: June 4, 2021

State of: Connecticut

County of: Hartford

Subscribed and sworn to before me this 4th day of June 2021

Notary Public:
My commission expires: 2/28/2025

JENIFER JODOIN
NOTARY PUBLIC
MY COMMISSION EXPIRES FEB. 28, 2025

ARCHITECTS/ENGINEER'S CERTIFICATE FOR PAYMENT

In accordance with the Contract Documents, based on the on-site observations and the data comprising this application, the Architect/Engineer certifies to the Owner/Client that to the best of the Architect's/Engineer's knowledge, information and belief that Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

AMOUNT CERTIFIED:

\$ 231,816.00

(Attach explanation if amount certified differs from the amount applied for. Initial all figures on this Application and on the Continuation Sheet that are changed to confirm to the amount certified)

ARCHITECT/ENGINEER:

By: _____

Date: _____

This certificate is not negotiable. The amount certified is payable only to the contract named herein. Issuance, payment and acceptance of payment are without prejudice to the rights of the Owner/Client or Contractor under this Contract.

CONTINUATION SHEET

DOCUMENT DETAIL SHEET

Document SUMMARY SHEET, APPLICATION AND CERTIFICATE FOR PAYMENT, containing Contractor's signed Certification is attached.
Use Column I on Contracts where variable retainage for line items apply.

APPLICATION NUMBER: 5
APPLICATION DATE: 05/31/2021
PERIOD: 05/01/21 - 05/31/21
ARCHITECTS/ENGINEERS PROJECT NO:

Contract Lines

A	B	C	D	E	F	G		H	I
ITEM NO.	DESCRIPTION OF WORK	SCHEDULED VALUE	WORK COMPLETED		MATERIALS PRESENTLY STORED (NOT IN D OR E)	TOTAL COMPLETED AND STORED TO DATE (D + E + F)	% (G / C)	BALANCE TO FINISH (C - G)	RETAINAGE
			FROM PREVIOUS APPLICATION (D + E)	THIS PERIOD					
1	BASE BID	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	100.00%	\$0.00	\$0.00
2	General Conditions	\$221,819.00	\$110,920.00	\$27,730.00	\$0.00	\$138,650.00	62.51%	\$83,169.00	\$6,932.50
3	02-070 Selective Demo	\$18,048.00	\$1,433.00	\$16,615.00	\$0.00	\$18,048.00	100.00%	\$0.00	\$902.40
4	02-080 Hazardous Abatement	\$19,932.00	\$1,995.00	\$17,937.00	\$0.00	\$19,932.00	100.00%	\$0.00	\$996.60
5	02-200 Earthwork	\$56,499.00	\$37,290.00	\$10,734.00	\$0.00	\$48,024.00	85.00%	\$8,475.00	\$2,401.20
6	03-003 Concrete	\$40,700.00	\$40,700.00	\$0.00	\$0.00	\$40,700.00	100.00%	\$0.00	\$2,035.00
7	04-200 Unit Masonry	\$79,518.00	\$73,157.00	\$6,361.00	\$0.00	\$79,518.00	100.00%	\$0.00	\$3,975.90
8	05-500 Metal Fabrications	\$4,313.00	\$4,313.00	\$0.00	\$0.00	\$4,313.00	100.00%	\$0.00	\$215.65
9	06-100 Rough Carpentry	\$55,658.00	\$40,829.00	\$12,047.00	\$0.00	\$52,876.00	95.00%	\$2,782.00	\$2,643.80
10	06-410 Custom Casework	\$10,761.00	\$5,381.00	\$1,507.00	\$0.00	\$6,888.00	64.01%	\$3,873.00	\$344.40
11	07-150 Dampproofing	\$2,094.00	\$2,094.00	\$0.00	\$0.00	\$2,094.00	100.00%	\$0.00	\$104.70
12	07-195 Air Barries	\$4,708.00	\$4,708.00	\$0.00	\$0.00	\$4,708.00	100.00%	\$0.00	\$235.40
13	07-200 Insulation	\$14,226.00	\$10,670.00	\$3,556.00	\$0.00	\$14,226.00	100.00%	\$0.00	\$711.30
14	07-470 Cement Board Siding	\$13,342.00	\$900.00	\$12,442.00	\$0.00	\$13,342.00	100.00%	\$0.00	\$667.10
15	07-500 Membrane Roofing	\$45,707.00	\$13,712.00	\$0.00	\$0.00	\$13,712.00	30.00%	\$31,995.00	\$685.60
16	08-100 Metal Door & Frames	\$19,865.00	\$17,000.00	\$2,865.00	\$0.00	\$19,865.00	100.00%	\$0.00	\$993.25
17	09-250 Gypsum Board	\$32,435.00	\$24,326.00	\$0.00	\$0.00	\$24,326.00	75.00%	\$8,109.00	\$1,216.30
18	09-310 Floor Finishes	\$23,881.00	\$19,105.00	\$955.00	\$0.00	\$20,060.00	84.00%	\$3,821.00	\$1,003.00
19	09-510 Acoustical Ceilings	\$12,451.00	\$6,226.00	\$0.00	\$0.00	\$6,226.00	50.00%	\$6,225.00	\$311.30
20	09-900 Painting	\$12,221.00	\$6,111.00	\$0.00	\$0.00	\$6,111.00	50.00%	\$6,110.00	\$305.55
21	10-000 Specialties	\$15,808.00	\$12,963.00	\$2,845.00	\$0.00	\$15,808.00	100.00%	\$0.00	\$790.40
22	15-300 Fire Protection	\$20,063.00	\$8,026.00	\$7,021.00	\$0.00	\$15,047.00	75.00%	\$5,016.00	\$752.35
23	15-400 Plumbing	\$102,757.00	\$71,930.00	\$28,827.00	\$0.00	\$100,757.00	98.05%	\$2,000.00	\$5,037.85
24	15-500 Heating & Air Conditioning	\$147,606.00	\$53,136.00	\$64,948.00	\$0.00	\$118,084.00	80.00%	\$29,522.00	\$5,904.20
25	16-001 Electrical	\$48,079.00	\$28,850.00	\$7,013.00	\$0.00	\$35,863.00	74.59%	\$12,216.00	\$1,793.15
26	ALTERNATE 5 (LINE 2)	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	100.00%	\$0.00	\$0.00
27	06-100 Rough Carpentry	\$68,745.00	\$50,193.00	\$15,114.00	\$0.00	\$65,307.00	95.00%	\$3,438.00	\$3,265.35
28	07-200 Insulation	\$2,895.00	\$2,171.00	\$724.00	\$0.00	\$2,895.00	100.00%	\$0.00	\$144.75
29	07-470 Cement Board Siding	\$3,000.00	\$3,000.00	\$0.00	\$0.00	\$3,000.00	100.00%	\$0.00	\$150.00
30	15-300 Fire Protection	\$7,360.00	\$2,944.00	\$2,576.00	\$0.00	\$5,820.00	75.00%	\$1,840.00	\$276.00
31	ALTERNATE 6 (LINE 3)	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	100.00%	\$0.00	\$0.00
32	16-001 Electrical	\$8,700.00	\$5,220.00	\$1,740.00	\$0.00	\$6,960.00	80.00%	\$1,740.00	\$348.00
TOTALS:		\$1,113,191.00	\$659,303.00	\$243,557.00	\$0.00	\$902,660.00	81.11%	\$210,331.00	\$45,143.00

CONTINUATION SHEET

DOCUMENT DETAIL SHEET

Change Orders

A	B	C	D	E	F	G	H	I	
ITEM NO.	DESCRIPTION OF WORK	SCHEDULED VALUE	WORK COMPLETED		MATERIALS PRESENTLY STORED (NOT IN D OR E)	TOTAL COMPLETED AND STORED TO DATE (D + E + F)	% (G / C)	BALANCE TO FINISH (C - G)	RETAINAGE
			FROM PREVIOUS APPLICATION (D + E)	THIS PERIOD					
33	PCCO#001								
33.1	PCCO#001 CE #001 - Sketch SK-A-1 Changes to Add Alt. #5	\$ (2,419.00)	\$0.00	\$460.00	\$0.00	\$460.00	-19.02%	\$ (2,879.00)	\$23.00
TOTALS:		\$ (2,419.00)	\$0.00	\$460.00	\$0.00	\$460.00	-19.02%	\$ (2,879.00)	\$23.00

Grand Totals

A	B	C	D		E	F	G		H	I
ITEM NO.	DESCRIPTION OF WORK	SCHEDULED VALUE	WORK COMPLETED		THIS PERIOD	MATERIALS PRESENTLY STORED (NOT IN D OR E)	TOTAL COMPLETED AND STORED TO DATE (D + E + F)	% (G / C)	BALANCE TO FINISH (C - G)	RETAINAGE
			FROM PREVIOUS APPLICATION (D + E)							
	GRAND TOTALS:	\$1,110,772.00	\$659,303.00		\$244,017.00	\$0.00	\$903,320.00	81.32%	\$207,452.00	\$45,166.00

DOCUMENT DETAIL SHEET - APPLICATION AND CERTIFICATE FOR PAYMENT

CONTRACTOR'S CERTIFICATION AND LIEN WAIVER AND SUBORDINATION

Application for Payment No. 05

TO: City of Middletown, Connecticut ("Owner")

FROM: Enterprise Builders, Inc. ("Contractor")

RE: Construction of South Fire District Building Renovations - PCD located at 445 Randolph Road, Middletown, CT 06457; (the "Project") owned by City of Middletown, Connecticut ("Owner")

DATE: 6/4/21

PERIOD: From 05/01/21 to 05/31/21

We are the general contractor for the Project, and we hereby certify as follows:

1. In reference to our contract dated December 3, 2020, with Owner for construction of the Project, and the Plans and Specifications therefor, no amendments, modifications or changes have been made with respect to our contract or the Plans and Specifications except such as have had your prior written approval. There are no pending change orders, except as follows: N/A

2. The present status of the account for this contract is as follows:

Original Contract Amt	\$ <u>1,113,191.00</u>	Work Completed through this Draw	\$ <u>903,320.00</u>
Change Orders	\$ <u>-2,419.00</u>	Prior Billings	\$ <u>626,338.00</u>
Revised Contract Amt	\$ <u>1,110,772.00</u>	Current Amount Owed	\$ <u>231,816.00</u>

The Application for Payment noted above is in compliance with the terms of our contract with Owner, and, upon the payment of the "Current Amount Owed" set forth above, we will have no other or additional claim (including claims for so called "extras") against Owner on account of our contract or otherwise for and through the period of time set forth above, for all labor and materials furnished by us through said period of time, except as follows:

(a) Retainage not exceeding 5.0 % of the value of labor and materials incorporated into the Project and retainage not exceeding 5.0 % of stored materials, and covered by applications submitted by us on account of the Project for which payment is to be made to us after substantial completion of our contract, as provided therein (the amount of said retainage, as of the end of the period of time set forth above is \$ 45,166.00 and

(b) (Please specify other claims, if any): N/A

3. The Owner is not in default of any of the Owner's obligations to us as of the date hereof, except as follows:

4. We have paid in full all of our obligations to subcontractors, workmen, suppliers and materialmen for and with respect to all labor and materials supplied through and including the date of our last Application for Payment, except for a retainage amount equal to % thereof, which we are holding in accordance with the terms of such obligations and our contract, and all our subcontractors have paid their subcontractors, workmen and materialmen in full for and with respect to all labor and materials supplied through and including the date of our last Application for Payment.

5. The undersigned hereby indemnifies and holds harmless Lender and Owner from and against any and all claims, damages, losses and expenses (including attorney's fees) resulting from (i) claims by any person who performed work or provided materials for the Project through the period of time set forth above by, through or under the undersigned and (ii) any breach of warranty or misrepresentation set forth herein.

6. The undersigned intends that this instrument shall release, discharge and dissolve any lien which the undersigned may now have or be entitled to have on account of work performed or materials furnished up to and including the period of time set forth above. If a lien or notice of intent to claim lien is filed by the undersigned on account of any of such work or materials, then the undersigned further hereby releases and terminates such lien or notice of intent to claim lien effective upon the recording of this instrument in the appropriate land records; provided, however, that any lien or notice of intent to claim lien filed with respect to any unpaid retainage amounts or disputed amounts set forth in paragraph 2 above shall not be released, but are hereby subordinated to any mortgage lien or security interest now or hereafter held by the Lender (and its successors and assigns) on the Project.

7. The undersigned further intends that this instrument shall subordinate any lien which the undersigned may hereafter be entitled to have on account of work performed or materials furnished after the period of time set forth above to any mortgage lien or security interest now or hereafter held by the Lender (and its successors and assigns) on the Project. If a lien or notice of intent to claim lien is filed by the undersigned on account of any of such work or materials, then the undersigned further hereby subordinates such lien or notice of intent to claim lien as aforesaid effective upon the recording of this instrument in the appropriate land records.

Executed this 4th day June, 2021

CONTRACTOR: Enterprise Builders, Inc.

By: _____
Name: Keith Czarnecki
Title: Principal

STATE of CONNECTICUT)

) SS: NEWINGTON

COUNTY of HARTFORD)

The foregoing instrument was acknowledged before me this 4th day of June, 2021 by: Keith Czarnecki, the Principal of Enterprise Builders, Inc., a corporation, on behalf of the corporation.



Commissioner of the Superior Court
Notary Public: Jenifer Jodoin
My Commission Expires: February 28, 2025

JENIFER JODOIN
NOTARY PUBLIC
MY COMMISSION EXPIRES FEB, 28, 2025

South Fire Addition & Renovations Potential Change Orders

June 14th 2021

Potential Change Orders	Cost/Credit	Estimated Cost	Purpose	Status
Enterprise Builders Inc.				
PCO #1 / CO #1 Removal of framing and supporting structure and the relocation of the ERV from the exterior to the interior.	(\$2,419.00)		Credit	Approved
PCO #2 Addition of Bunk Cubicles in the Dormitory.	\$30,003.38		Betterment	Rejected
PCO #3 / CO #2 Addition of 2 CO Detectors & 4 Smoke Detectors.	\$4,215.00		Betterment	Approved Processing
PCO #4 / CO #3 Addition of Solartube Daylighting in the lounge.	\$8,849.75		Betterment	Approved Processing
PCO #5 / CO #2 Removing the washer & dryer hookups from project.	(\$807.00)		Credit	Approved Processing
PCO #6 / CO #2 Fan Coil Units (AC) for front offices.	\$12,091.00		Betterment	Approved Processing
PCO #7 / CO #2 Provide temporary power to phase I work while awaiting approval of code modification from the state for elec. panel.	\$3,292.00		Necessity	Approved Processing
PCO #8 / CO #2 Outlet & Relocation of HDMI	\$917.00		Betterment	Approved Processing
PCO #9 / CO #2 IT Cabinet and installation for server rm.	\$1,396.00		Betterment	Approved Processing
PCO #10 Demolition of existing partition in lounge	\$11,041.00		Betterment	Rejected
PCO #11 / CO #2 Painting of Bunk Cubicles.	\$525.00		Betterment	Approved Processing

PCO #12 Painting and new flooring in existing east wing areas.	\$9,866.00	Betterment	Pending
PCO #13 / CO #3 Provide working platform in existing electrical room. Pending approval of code modification.	\$1,123.50	Necessity	Approved Processing
PCO #14 / CO #3 Furr out existing masonry wall at new north hallway.	\$2,990.00	Betterment	Approved Processing
PCO #15 / CO #3 4 Additional lockers to replace double lockers.	\$2,035.00	Betterment	Approved Processing
Additional Work #1 (Salafia Electric, LLC) Addition of two electrical exterior outlets.	\$1,660.00	Betterment	Approved
Additional Work #2 (Salafia Electric, LLC) Notification lights & speakers for when there is a call.	\$5,835.00	Necessity	Approved
Additional Work #3 Addition of Bunk Cubicles in the Dormitory w/o painting.	\$6,800.00	Betterment	Approved
Special Testing #1 Phase I air testing after abatement.	\$550.00	Necessity	Approved
Special Testing #2 Phase II air testing after abatement.	\$1,260.00	Necessity	Approved

Total of Credits (Approved, Estimated & Proposed)	(\$3,226.00)
Total Additional Cost (Approved, Estimated & Proposed)	\$63,405.25
Net Additional Cost (Approved, Estimated & Proposed)	<u>\$60,179.25</u>

Approved Total of Credits	(\$3,226.00)
Approved Total Additional Cost	\$53,539.25
Net Approved Additional Cost	<u>\$50,313.25</u>

Summary of Funds

Grant Amount	\$1,000,000.00
State Fees	\$5,000.00
Professional Fees:	
Initial Design - Architectural, Estimating & Engineering	\$49,000.00
Re-Design Architectural, Estimating & Engineering	\$40,500.00
Construction Administration (billed during construction)	\$10,000.00
Environmental Testing	\$6,200.00
	<hr/>
	\$105,700.00
Zoning Variance Process	\$435.34
	<hr/>
Remaining Grant Funds	\$888,864.66
Additional Funds from South Fire	\$332,273.00
	<hr/>
Total Funds for Construction	\$1,221,137.66

Construction Costs, with Enterprise as Lowest Responsible Bidder

Base Bid	\$1,022,491.00
Add Alternates:	
Rear Pitched Roof	\$82,000.00
Data/Comm. Setup	\$8,700.00
	<hr/>
	\$90,700.00

Total Construction Cost	\$1,113,191.00
-------------------------	----------------

Total Contingency	\$107,946.66
Remaining Funds(Assuming all Change Orders are Accepted)	\$47,767.41



Prime Contract Potential Change Order
#004-R3: CE #006 - Solartube Daylighting

Created on: 5/5 /2021
Project Name: South Fire District Renovations and Addition
Project Number: 538

TO:

City of Middletown
245 Dekoven Drive
Middletown Connecticut, 06457

PROJECT:

South Fire District Renovations and Addition
445 Randolph Road
Middletown, Connecticut 06457

REQUEST RECEIVED FROM:

LOCATION:

FROM:

Enterprise Builders, Inc.
46 Shepard Drive
Newington Connecticut, 06111

CONTRACT:

1 - South Fire District Prime Contract

STATUS:

Pending - In Review

ACCOUNTING METHOD:

Amount Based

TOTAL AMOUNT:

\$8,849.75

POTENTIAL CHANGE ORDER TITLE: CE #006 - Solartube Daylighting

CHANGE REASON: Owner

POTENTIAL CHANGE ORDER DESCRIPTION: *(The Contract Is Changed As Follows)*

CE #006 - Solartube Daylighting

Owner requested to Install Two (2) Solartube in the Lounge (phase two)

REFERENCES / ATTACHMENTS:

[JHS Change Order Proposal dated 2021-05-17 - NEW.pdf](#) [Willco Quote dated 2021-05-17 - NEW.pdf](#) [M Pienkos Quote dated 2021-03-17 - NEW.pdf](#)

SCHEDULE IMPACT: 0 days

#	SubJob	Cost Code	Description	Type	Amount
1	N/A	6-06-100 - Rough Carpentry	M Pienkos: Install two (2) solartube (Ref. M. Pienkos Email dated 3/17/21)	Subcontract	\$ 2,000.00
2	N/A	7-07-500 - Membrane Roofing	JHS: Install flange for solar tube and provide underlayment and shingles (Ref. JHS COP dated 5/17/21)	Subcontract	\$ 3,059.00
3	N/A	10-10-700 - Ext. Protection Devices Opens	Willco: Supply tubular daylighting device. (Ref. Willco quote dated 5/17/21)	Subcontract	\$ 3,370.00
Subtotal:					\$8,429.00
	20-001-0 EBI: 5% OH&P (1/01-175-O): ≈ 4.99% Applies to Materials, Commitment, Allowances, Subcontract, and Labor.				\$ 420.75
Grand Total:					\$8,849.75



Enterprise Builders, Inc.

By

Date

Approved on behalf of City of Middletown

By

Date

Affirmative Action / Equal Opportunity Employer



170 Strong Road
South Windsor CT 06074
860-757-3870



Change Order Proposal

Proposal Date: May 17, 2021
Site: South Fire District Middletown, CT

BID SPECIFICATIONS

SCOPE OF WORK

PROVIDE ALL SAFETY, LABOR AND MATERIAL TO PERFORM THIS SCOPE OF WORK.

- Furnish & Install safety equipment in accordance to OSHA guidelines and JHS Restoration Site Specific Safety Plan.
- Installation of flange for Solar Tube at two locations
- Provide underlayment's, and shingles

INVESTMENT

Installation of Solar tube Flange \$3,059.00

JHS Restoration, Inc.
AA/EOE Employer
State of CT DAS Certified Woman Owned Minority Company

Exclusions:

Taxes, Permits, Bonds, Existing Roof Demolition, Carpentry work, Wood Blocking, Plywood Deck Replacement, Skylights, Soffits and Fascia work, Flashings not contiguous with roofing, Temporary Roofing, Phased Roofing Work, Removal of Snow & Ice / Ponding water, Overtime / Off-Hour Work, Asbestos or Hazardous Material Removal/Disposal

SUMMARY

Thank you for the opportunity to bid on this project. Please contact me upon review so that I may address any questions or concerns you have and to discuss any options or changes that may come up. You may contact me directly at (860) 757-3870.

John Snyder
Vice President

ACCEPTANCE OF PROPOSAL

THE ABOVE PRICES, SPECIFICATIONS AND CONDITIONS ARE SATISFACTORY AND ARE HEREBY ACCEPTED. YOU ARE AUTHORIZED TO DO THE WORK, AS SPECIFIED. PAYMENT WILL BE MADE AS OUTLINED ABOVE. A 1% (12% apr) LATE FEE WILL BE CHARGED ON ALL UNPAID BALANCES OVER 30 DAYS. IN EVENT OF DEFAULT BY BUYER, BUYER AGREES TO PAY ALL COST OF COLLECTION INCLUDING REASONABLE ATTORNEYS FEES IN ADDITION TO OTHER DAMAGES INCURRED BY SELLER

Authorized Signature _____ DATE

JHS Acceptance _____ DATE

JHS Restoration, Inc.
AA/EOE Employer
State of CT DAS Certified Woman Owned Minority Company

Mazzetti, Christian

From: Mirosław Pienkos <mpienkosllc@gmail.com>
Sent: Wednesday, March 17, 2021 5:23 PM
To: Mazzetti, Christian
Subject: Solatube labor cost

Follow Up Flag: Follow up
Flag Status: Flagged

Pienkos contracting LLC

South fire district

Install two Solatube
Labor cost \$ 2,000

3/17/21

Mirosław Pienkos

Sent from my iPad



BID QUOTE

TO: Enterprise Builders Inc.
Attention: Christian Mazetti,
46 Shepard Drive
Newington, CT 06111-

DATE: 5/17/2021
RE: South Fire District Bldg.
Middletown, CT
ARCHITECT: Landmark Architects, P.C.
SECTION: Tubular Daylighting Device

Dear Christian:

We propose to Deliver Only the following items according to the following terms and conditions:

Quotation Details

SOLATUBE TUBULAR DAYLIGHTING DEVICE

**TWO (2) S750DSC-DAI - F8 FI MR-E5 AK -TM L1 LN -I
EACH CONSISTS OF:**

**750 DS DOME & TUBE RING KIT
750 DS INNER DOME ACRYLIC
750 DS FLASHING 8" NO PITCH
ROOFING SEALANT
750 DS EXT TUBE 24" LENGTH (5)
750 DS TOP/BOTTOM ANGLE KIT
750 DS FLASHING INSULATOR
750 DS-C METAL TRANSITION DIFFUSER KIT OPTIVIEW
750 DS-C NATURAL EFFECT LENS FOR METAL TRANSITION BOX**

**GRAND TOTAL \$3,370.00
Tax Exempt**

50% TO ORDER / 50% UPON CONFIRMATION OF SHIPPING

Notes:

**Solatubes mounts onto a shingle roof
Total includes freight
All sales are final**

INSURANCE Coverage: Willco Sales Service, Inc. standard insurance coverage and blanket endorsement CG D2 46 apply. Additional policies or coverage are not included. BOND: Add 3% to contract total.

Excluded Unloading and Carry-In; Inspection; Freight Damage; Installation;

BID QUOTE Continued...

TO: Enterprise Builders Inc.
46 Shepard Drive
Newington, CT 06111-

DATE: 5/17/2021
RE: South Fire District Bldg.

Above price is good for 30 days from date of quote.
Payments for goods and services are due upon completion of
work unless otherwise specified. Interest shall be added at
the rate of 1.5% per month on the unpaid balance of any
account past due. Purchaser shall pay all costs of
collections, including a reasonable attorney's fee, on any
accounts past due.

ACCEPTED BY: _____

DATE: _____

Willco Sales & Service, Inc.

BY: _____
Scott Gineo



Prime Contract Potential Change Order
#011: CE #014 - Frame Platform in Electrical Room

Created on: 5/25 /2021
Project Name: South Fire District Renovations and Addition
Project Number: 538

TO:

City of Middletown
245 Dekoven Drive
Middletown Connecticut, 06457

PROJECT:

South Fire District Renovations and Addition
445 Randolph Road
Middletown, Connecticut 06457

REQUEST RECEIVED FROM:

LOCATION:

FROM:

Enterprise Builders, Inc.
46 Shepard Drive
Newington Connecticut, 06111

CONTRACT:

1 - South Fire District Prime Contract

STATUS:

Draft

ACCOUNTING METHOD:

Amount Based

TOTAL AMOUNT:

\$1,123.50

POTENTIAL CHANGE ORDER TITLE: CE #014 - Frame Platform in Electrical Room

CHANGE REASON: Design Team

POTENTIAL CHANGE ORDER DESCRIPTION: *(The Contract Is Changed As Follows)*

CE #014 - Frame Platform in Electrical Room

Design Team received a Code Modification that allows a height of 7' above a working platform.
Need to provide a working platform in the existing electrical room to bring the floor surface up 7"

REFERENCES / ATTACHMENTS:

[M Pienkos Cost 05-21-21.pdf](#) [538 RFI 008 Existing Electrical Room Size Response 05-13-21.pdf](#)

SCHEDULE IMPACT: 0 days

#	SubJob	Cost Code	Description	Type	Amount
1	N/A	6-06-100 - Rough Carpentry	M. Pienkos: Frame 7' x 10' platform with 2 x 6 pressure treated wood and two layers 3/4" plywood per email dated 5/21/21	Subcontract	\$ 1,070.00
Subtotal:					\$1,070.00
	20-001-0 EBI: 5% OH&P (1/01-175-O): 5.00% Applies to Materials, Commitment, Allowances, Subcontract, and Labor.				\$ 53.50
Grand Total:					\$1,123.50



Enterprise Builders, Inc.

By

Date

Approved on behalf of City of Middletown

By

Date

Affirmative Action / Equal Opportunity Employer

From: Miroslaw Pienkos [mailto:mpienkosllc@gmail.com]

Sent: Friday, May 21, 2021 5:23 PM

To: Mazzetti, Christian

Subject: Frame platform in electrical room

Pienkos contracting LLC

South fire district

Frame 7' x 10' platform with 2 x 6 pressure treated wood and two layers 3/4" plywood

Labor cost \$ 400

Material cost \$ 670

Total cost \$ 1070

5/21/21

Miroslaw Pienkos

Sent from my iPad



Enterprise Builders, Inc.
46 Shepard Drive
Newington, Connecticut 06111
Phone: (860) 466-5188
Fax: (860) 466-4119

Project: 538 - South Fire District Renovations and Addition
445 Randolph Road
Middletown, Connecticut 06457

Existing Electrical Room Size

TO:	Paul Morin (Landmark Architects, P.C.)	FROM:	Brittany Ferro (K-Co Electric, LLC) P.O Box 7032 Plainville, Connecticut 06062-7032
CREATED DATE:	03/03/ 2021	STATUS:	Open
LOCATION:		DUE DATE:	03/07/2021
COST CODE:		REFERENCE:	
COST IMPACT:	TBD	SCHEDULE IMPACT:	TBD
DRAWING NUMBER:	E - 1.2	SPEC SECTION:	
RECEIVED FROM:	Brittany Ferro (K-Co Electric, LLC)		
COPIES TO:	Brittany Ferro (K-Co Electric, LLC), File (Enterprise Builders, Inc.), Christian Mazzetti (Enterprise Builders, Inc.), Kyle Richard (Enterprise Builders, Inc.)		

Question from Brittany Ferro (K-Co Electric, LLC) at 04:04 PM on 03/03/2021

RFI: Existing Electrical room size.

Good Afternoon,

Panel DP shown on E-1.2 and listed with the power riser diagram on E-2.1 show the new panel to be installed labeled DP. After yesterday's job site meeting I noticed the approved submittal panel on site. After taking measurements, the means to shut off breakers will not meet code. I checked in with multiple vendors to see what options we might have. It appears there is not a 400 AMP panel that will house all the breakers required for the project. The electrical DP panel will not fit in the existing electrical room due to height. The panel height is 90" overall. The first breaker is located 5'10" from the bottom of the panel. With the existing trough, the new panel would have to be mounted 21" off the floor putting the highest breaker at 7'-7" off the floor. This is higher than required by code. Please advise.

Attachments:

Response from Paul Morin (Landmark Architects, P.C.) at 09:45 AM on 05/13/2021

We received a code modification that allows a height of 7' above a working platform. Provide a working platform in the existing electrical room to bring the floor surface up 7".

Attachments:

[21-0287 MIDDLETOWN 445 Randolph Road.pdf](#) [SK-A-3 Working Platform.pdf](#)

Response from Paul Morin (Landmark Architects, P.C.) at 12:18 PM on 04/01/2021

See attached document.


Attachments:

[538-South_Fire_District_Renovations_and_Addition-8-Existing_Electrical_Room_Size-2021-03-04 - IES ANSWER.pdf](#)

BY

DATE

COPIES TO

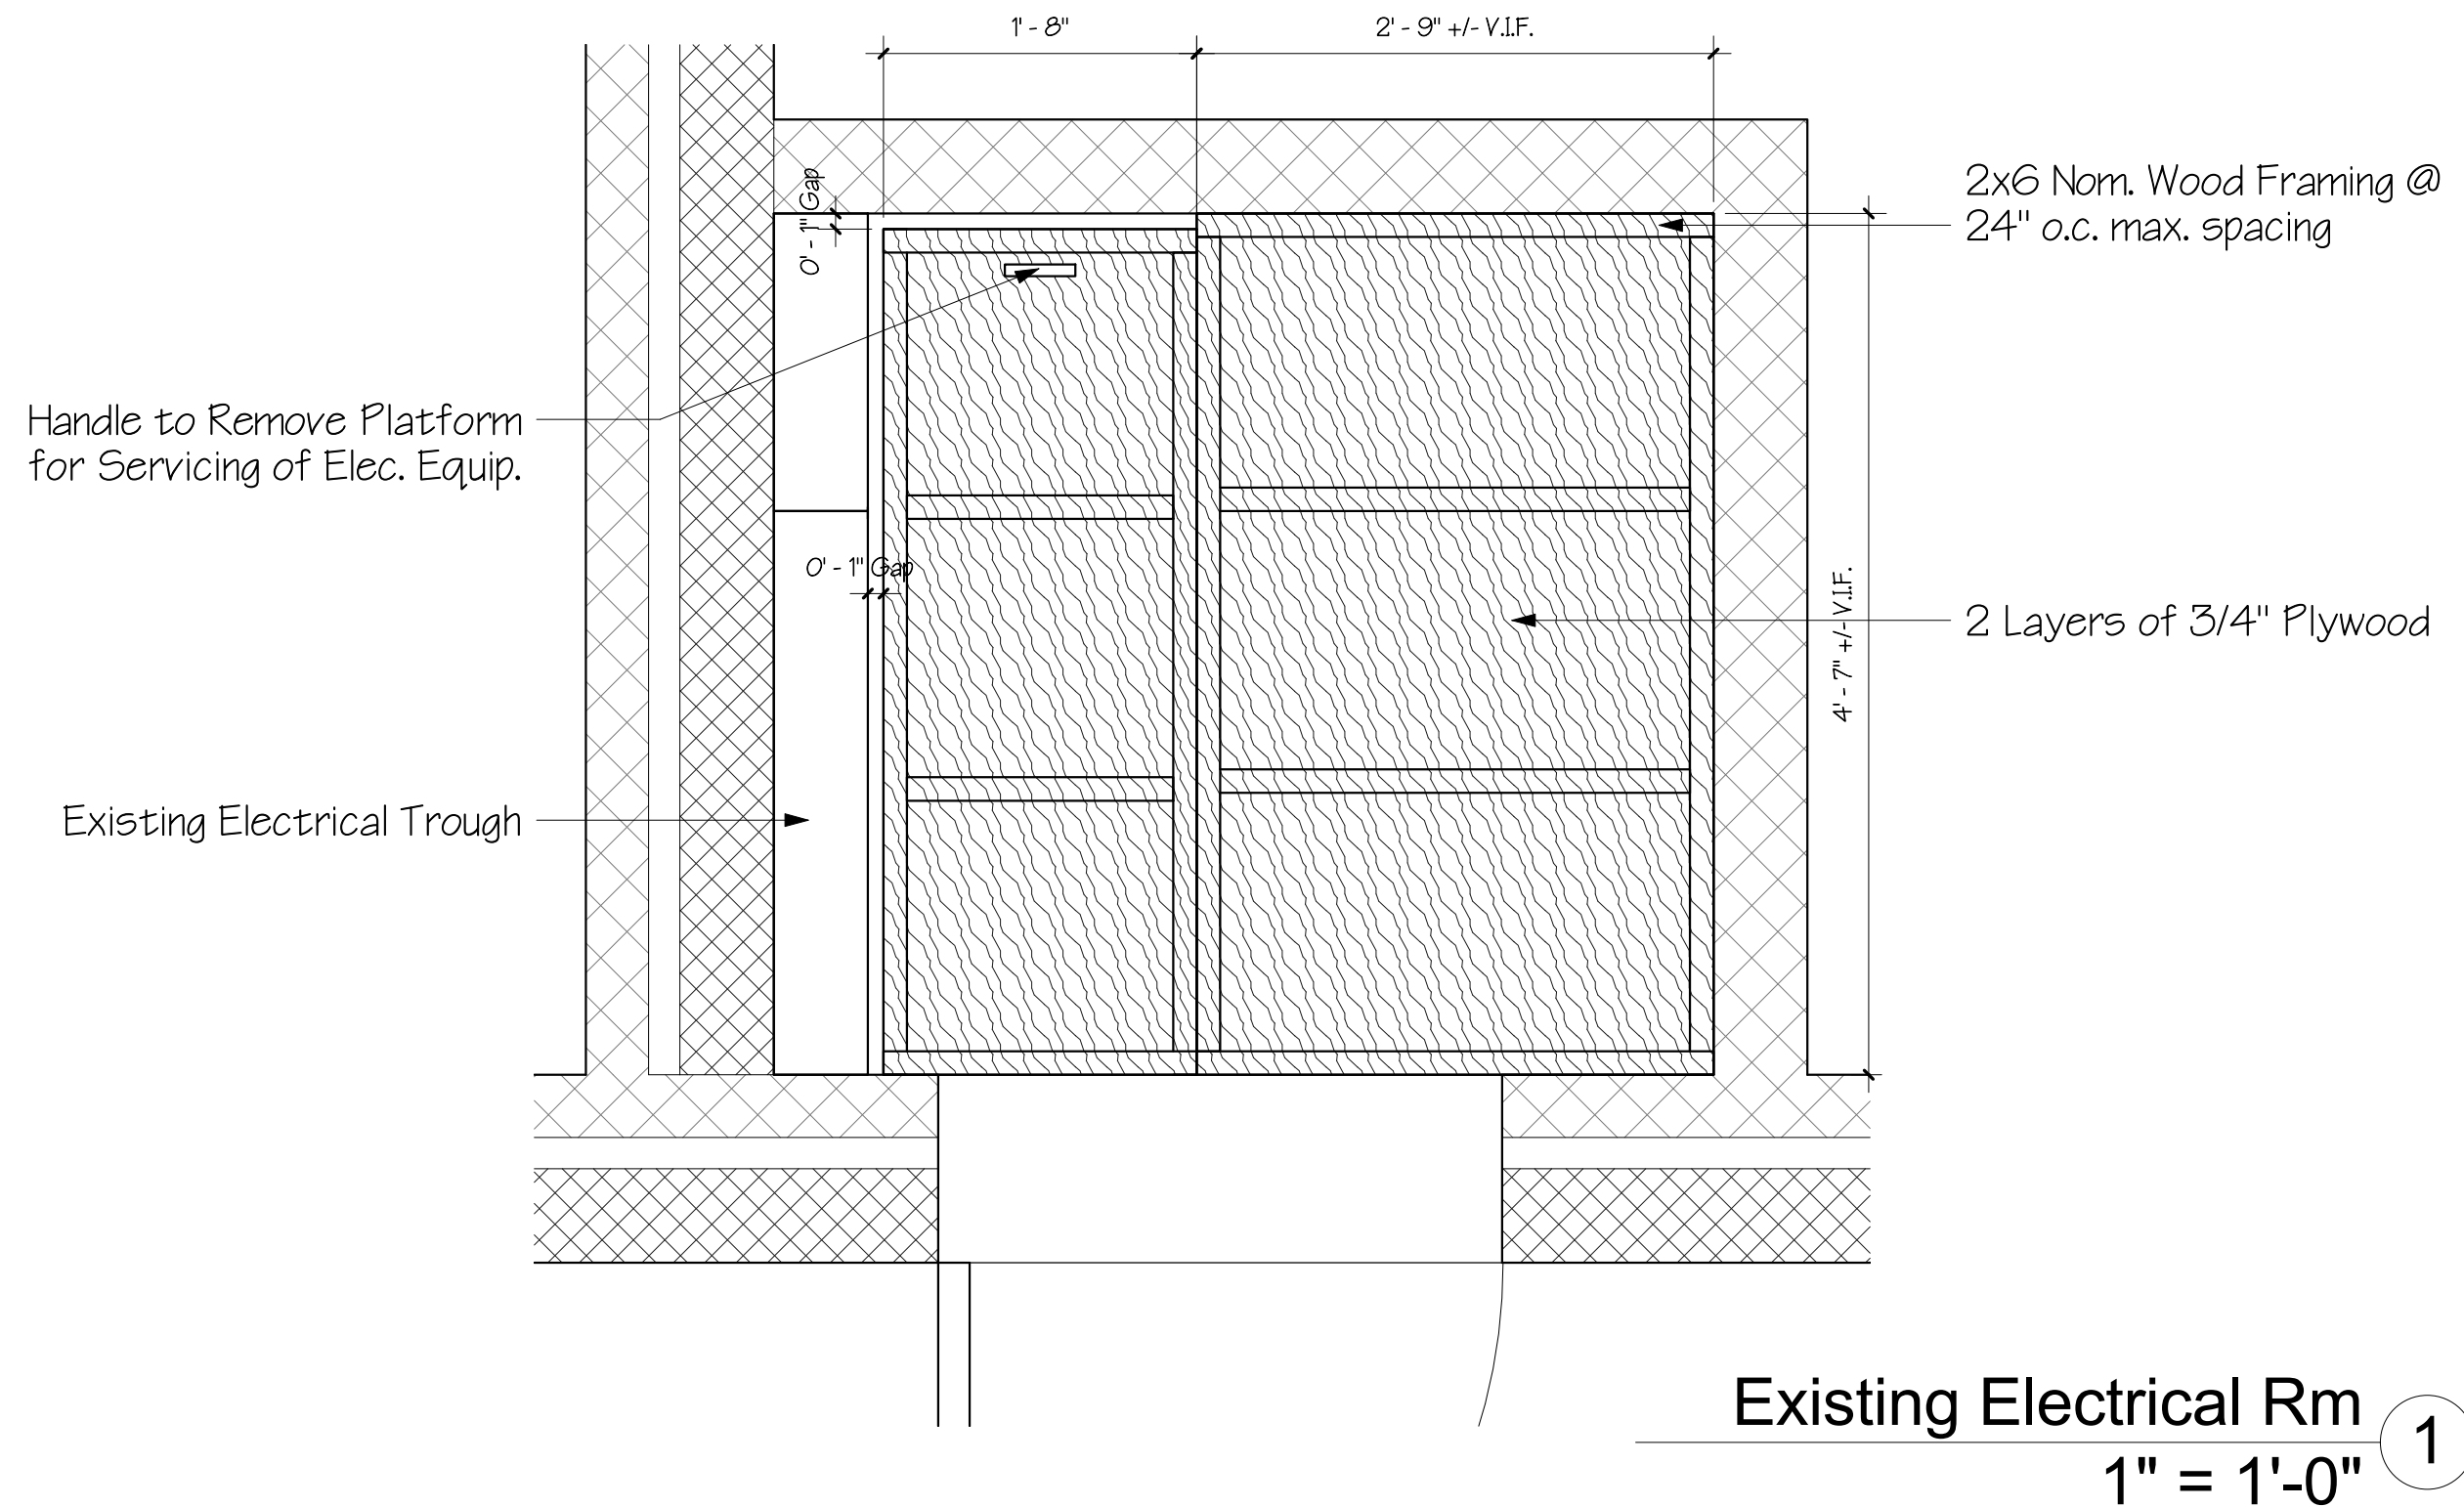

City of Middletown
South Fire District Bldg Renovations & Addition



Elec. Rm Working Platform

Project number A18005
Date 5/11/2021
Drawn by Paul Morin

SK-A-3

Scale 1" = 1'-0"



Office of the State Building Inspector

May 11, 2021

Paul Pizzo
Landmark Architects, PC
100 Riverview Center, Suite 204
Middletown, CT

Email: ppizzo@landmarkarch.com

Request for Modification of the 2018 Connecticut State Building Code
Subject Property: 445 Randolph Road, Middletown
CASE NUMBER: M-21-0287

Dear Mr. Pizzo,

I have reviewed your request for modification of Article 240.24(A) of the 2017 National Electrical Code portion of the 2018 Connecticut State Building Code which states:

(A) Accessibility. Switches containing fuses and circuit breakers shall be readily accessible and installed so that the center of the grip of the operating handle of the switch or circuit breaker, when in its highest position, is not more than 2.0 m (6 ft 7 in.) above the floor or working platform, unless one of the following applies:

Modification requested:

To allow a new 400A panel replacing an existing 225A panel to have a top breaker with a height of 7'0" above the floor. An existing wire trough under the panel precludes lowering the panel.

Decision: APPROVED.

The approval of this modification, to allow the location of this panel as described, is based on existing conditions that preclude strict compliance with the requirements for new construction.

This modification is specific to the subject property and the circumstances identified in your application. If you have any questions, please contact me at 860-713-5900.

Sincerely,

Joseph V. Cassidy, P.E.
State Building Inspector

C: Darren Hobbs, Deputy State Building Inspector
Dean Lisitano, Middletown Building Official



Prime Contract Potential Change Order
#012: CE #015 - Replace Flooring and Re-Paint
Existing Hallway

Created on: 5/28 /2021
Project Name: South Fire District Renovations and Addition
Project Number: 538

TO:

City of Middletown
245 Dekoven Drive
Middletown Connecticut, 06457

PROJECT:

South Fire District Renovations and Addition
445 Randolph Road
Middletown, Connecticut 06457

REQUEST RECEIVED FROM:

LOCATION:

FROM:

Enterprise Builders, Inc.
46 Shepard Drive
Newington Connecticut, 06111

CONTRACT:

1 - South Fire District Prime Contract

STATUS:

Draft

ACCOUNTING METHOD:

Amount Based

TOTAL AMOUNT:

\$9,866.00

POTENTIAL CHANGE ORDER TITLE: CE #015 - Replace Flooring and Re-Paint Existing Hallway

CHANGE REASON: Owner

POTENTIAL CHANGE ORDER DESCRIPTION: *(The Contract Is Changed As Follows)*

CE #015 - Replace Flooring and Re-Paint Existing Hallway
Owner wants to replace the flooring & repaint the existing hallway

REFERENCES / ATTACHMENTS:

[538 - A-1.1 Proposed Plan WITH EBI NOTES 05-21-21.pdf](#) [Fire District.pdf](#) [S F CO proposal hallway flooring OPT2.pdf](#) [Div 09 - Painting.pdf](#)

SCHEDULE IMPACT: 0 days

#	SubJob	Cost Code	Description	Type	Amount
1	N/A	2-02-080 - Hazardous Material Abatement	GE Construction:Remove carpet, VCT & mastic as ACM under full containment	Subcontract	\$ 6,750.00
2	N/A	9-09-310 - Ceramic Tile	Barall & Konover:Replace Flooring at Existing Hallway	Subcontract	\$ 1,046.00
3	N/A	9-09-900 - Painting	Superior Painting: Paint Existing Corridor Walls	Subcontract	\$ 1,600.00
Subtotal:					\$9,396.00
20-001-0 EBI: 5% OH&P (1/01-175-O): 5.00% Applies to Materials, Commitment, Allowances, Subcontract, and Labor.					\$ 470.00
Grand Total:					\$9,866.00



Enterprise Builders, Inc.

By

Date

Approved on behalf of City of Middletown

By

Date

Affirmative Action / Equal Opportunity Employer

CHANGE ORDER PROPOSAL WORKSHEET

To: Enterprise Builders **From:** GE Construction LLC

Project: Southfire District **Date:** 5/24/2021

Middletown CT **PCO/RFQ#:** Remove flooring on hallway

Description: Remove carpet, VCT & mastic as ACM under full containment

Quant.	Unit	Description of Material and Equipment (attached list if req'd)	Unit Cost	
1		Mobilization	\$ 250.00	\$ 250.00
1		Set up full containment (small, including equipment & supplies)	\$ 2,250.00	\$ 2,250.00
1		Remove carpet, VCT & mastic	\$ 2,000.00	\$ 2,000.00
1		take down containment once air test pass	\$ 1,000.00	\$ 1,000.00
1		disposal of ACM waste	\$ 400.00	\$ 400.00
Line #1 Material and Equipment Subtotal				

Crew	Labor Classification	Hours	Base Rate	Fringe	Unem ins	Liability	Wrkrs Comp.	fica	Total
3	#1 common Labor	60	\$ 31.00	22.15	2.15	\$ 4.05	15.75	\$ 6.50	
									\$ -
									\$ -
									\$ -
									\$ -
Line #2 Labor Subtotal									

Line #3 Total Labor, Materials and Equipment	\$ 5,900.00
---	--------------------

Line #3 Amt	Overhead and Profit % Mark-up on Own Work	Allow %	Applicable %	Total
	Total From Line #3		15%	\$ 885.00
Line #4 Total Mark-up on Contractor's Own Work				

Subcontractor Cost (from attached subcontractors' change order proposal worksheet form)		
Trade	Name of Subcontractor	Total
		\$ -
		\$ -
		\$ -
Line #5 Subcontractor Total		

Line #6 Contractor's Mark-up on Subcontractor Work (see note below)	\$ -
--	-------------

Line #7 Total Proposed Change Order Amount	6,750.00
---	-----------------



BARALL & KONOVER FLOORS
"If it covers a floor, we have it!"

714 Blue Hills Avenue. Hartford, CT 06112 • bill@bkfloors.com • Phone: (860) 242-5200 • Fax: (860)-286-0016

Date: May 21, 2021

Attn: Christian Mazzetti

Re: South Fire District
Flooring Proposal – R1

Christian,

Thank you for the opportunity to submit our proposal for:

REPLACE FLOORING AT EXISTING HALLWAY for the total sum of \$ 1,046.00
ONE THOUSAND FOURTY-SIX and no/100 DOLLARS

Qualification: Price includes floor preparation up to 1/16".

Price includes floor installation for area at new drawing issue 5-21-21

We will be available to discuss any concerns you may have at your convenience.

Very truly yours,

BARALL & KONOVER FLOORS INC.

Jessica Canchanya

Superior Painting LLC

66 Borghesi CT
Wolcott, CT 06716
P 203-441-4089 F 203 441-4124
HIC# 0624098
superiorpaintingllc@comcast.net
DAS SBE certified

CHANGE ORDER PROPOSAL

Date: 4/20/21

To: Estimating

Attn:

Fax:

From: Robert Sanseverino

We are pleased to submit our proposal for 09910 Painting

PROJECT: South Fire District


Base Price: 1,600.00

Scope:

Paint Existing Corridor Walls
Labor 16 hours 1,200.00
Material 400.00

Open Shop

Superior Finishes at Affordable pricing



General Notes	Wall Type Legend	Symbol/Tag Legend	Name Elevation	Level Elevation
<div>YELLOW</div> <p>Provide drawings for masonry partitions and arches per specifications.</p> <p>Provide partition features. Include partition drawings for details.</p> <p>Provide moisture resistance GMB at wet walls in kitchen & bathrooms.</p> <p>Provide floor finishes and replace existing floors where noted in finish schedule, see sheet A-7.2.</p> <p>Provide 1" x 3" x 5" GMB for all walls typical.</p> <p>Provide light fixtures, exhaust fans, outlets & switches indicated. See electrical drawings.</p> <p>Refer to structural drawings for size & locations of structural members.</p> <p>Provide a structural drawing for size & locations of structural members.</p> <p>Dimensions are to the face of structural wall elements (CMU, face of concrete, etc.) unless noted otherwise.</p> <p>Existing loads and CMU in the core (excluding air in main lines) must be determined.</p> <p>Construction must be coordinated with the owner's rep. in order not to disturb the day to day operations of the fire station.</p> <p>Doors to be at or adjacent wall surface, except doors which are to be centered.</p>	<p>FLURRING Type Mark: PARTITION Fire Rating Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (UL DOCS WHERE NOTED) 17hr (UL DOCS WHERE NOTED) 18hr (UL DOCS WHERE NOTED) 19hr (UL DOCS WHERE NOTED) 20hr (UL DOCS WHERE NOTED) 21hr (UL DOCS WHERE NOTED) 22hr (UL DOCS WHERE NOTED) 23hr (UL DOCS WHERE NOTED) 24hr (UL DOCS WHERE NOTED) 25hr (UL DOCS WHERE NOTED) 26hr (UL DOCS WHERE NOTED) 27hr (UL DOCS WHERE NOTED) 28hr (UL DOCS WHERE NOTED) 29hr (UL DOCS WHERE NOTED) 30hr (UL DOCS WHERE NOTED) 31hr (UL DOCS WHERE NOTED) 32hr (UL DOCS WHERE NOTED) 33hr (UL DOCS WHERE NOTED) 34hr (UL DOCS WHERE NOTED) 35hr (UL DOCS WHERE NOTED) 36hr (UL DOCS WHERE NOTED) 37hr (UL DOCS WHERE NOTED) 38hr (UL DOCS WHERE NOTED) 39hr (UL DOCS WHERE NOTED) 40hr (UL DOCS WHERE NOTED) 41hr (UL DOCS WHERE NOTED) 42hr (UL DOCS WHERE NOTED) 43hr (UL DOCS WHERE NOTED) 44hr (UL DOCS WHERE NOTED) 45hr (UL DOCS WHERE NOTED) 46hr (UL DOCS WHERE NOTED) 47hr (UL DOCS WHERE NOTED) 48hr (UL DOCS WHERE NOTED) 49hr (UL DOCS WHERE NOTED) 50hr (UL DOCS WHERE NOTED) 51hr (UL DOCS WHERE NOTED) 52hr (UL DOCS WHERE NOTED) 53hr (UL DOCS WHERE NOTED) 54hr (UL DOCS WHERE NOTED) 55hr (UL DOCS WHERE NOTED) 56hr (UL DOCS WHERE NOTED) 57hr (UL DOCS WHERE NOTED) 58hr (UL DOCS WHERE NOTED) 59hr (UL DOCS WHERE NOTED) 60hr (UL DOCS WHERE NOTED) 61hr (UL DOCS WHERE NOTED) 62hr (UL DOCS WHERE NOTED) 63hr (UL DOCS WHERE NOTED) 64hr (UL DOCS WHERE NOTED) 65hr (UL DOCS WHERE NOTED) 66hr (UL DOCS WHERE NOTED) 67hr (UL DOCS WHERE NOTED) 68hr (UL DOCS WHERE NOTED) 69hr (UL DOCS WHERE NOTED) 70hr (UL DOCS WHERE NOTED) 71hr (UL DOCS WHERE NOTED) 72hr (UL DOCS WHERE NOTED) 73hr (UL DOCS WHERE NOTED) 74hr (UL DOCS WHERE NOTED) 75hr (UL DOCS WHERE NOTED) 76hr (UL DOCS WHERE NOTED) 77hr (UL DOCS WHERE NOTED) 78hr (UL DOCS WHERE NOTED) 79hr (UL DOCS WHERE NOTED) 80hr (UL DOCS WHERE NOTED) 81hr (UL DOCS WHERE NOTED) 82hr (UL DOCS WHERE NOTED) 83hr (UL DOCS WHERE NOTED) 84hr (UL DOCS WHERE NOTED) 85hr (UL DOCS WHERE NOTED) 86hr (UL DOCS WHERE NOTED) 87hr (UL DOCS WHERE NOTED) 88hr (UL DOCS WHERE NOTED) 89hr (UL DOCS WHERE NOTED) 90hr (UL DOCS WHERE NOTED) 91hr (UL DOCS WHERE NOTED) 92hr (UL DOCS WHERE NOTED) 93hr (UL DOCS WHERE NOTED) 94hr (UL DOCS WHERE NOTED) 95hr (UL DOCS WHERE NOTED) 96hr (UL DOCS WHERE NOTED) 97hr (UL DOCS WHERE NOTED) 98hr (UL DOCS WHERE NOTED) 99hr (UL DOCS WHERE NOTED) 100hr (UL DOCS WHERE NOTED)</p> <p>EXTERIOR MASONRY WALL (LB) Fire Rating Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (UL DOCS WHERE NOTED) 17hr (UL DOCS WHERE NOTED) 18hr (UL DOCS WHERE NOTED) 19hr (UL DOCS WHERE NOTED) 20hr (UL DOCS WHERE NOTED) 21hr (UL DOCS WHERE NOTED) 22hr (UL DOCS WHERE NOTED) 23hr (UL DOCS WHERE NOTED) 24hr (UL DOCS WHERE NOTED) 25hr (UL DOCS WHERE NOTED) 26hr (UL DOCS WHERE NOTED) 27hr (UL DOCS WHERE NOTED) 28hr (UL DOCS WHERE NOTED) 29hr (UL DOCS WHERE NOTED) 30hr (UL DOCS WHERE NOTED) 31hr (UL DOCS WHERE NOTED) 32hr (UL DOCS WHERE NOTED) 33hr (UL DOCS WHERE NOTED) 34hr (UL DOCS WHERE NOTED) 35hr (UL DOCS WHERE NOTED) 36hr (UL DOCS WHERE NOTED) 37hr (UL DOCS WHERE NOTED) 38hr (UL DOCS WHERE NOTED) 39hr (UL DOCS WHERE NOTED) 40hr (UL DOCS WHERE NOTED) 41hr (UL DOCS WHERE NOTED) 42hr (UL DOCS WHERE NOTED) 43hr (UL DOCS WHERE NOTED) 44hr (UL DOCS WHERE NOTED) 45hr (UL DOCS WHERE NOTED) 46hr (UL DOCS WHERE NOTED) 47hr (UL DOCS WHERE NOTED) 48hr (UL DOCS WHERE NOTED) 49hr (UL DOCS WHERE NOTED) 50hr (UL DOCS WHERE NOTED) 51hr (UL DOCS WHERE NOTED) 52hr (UL DOCS WHERE NOTED) 53hr (UL DOCS WHERE NOTED) 54hr (UL DOCS WHERE NOTED) 55hr (UL DOCS WHERE NOTED) 56hr (UL DOCS WHERE NOTED) 57hr (UL DOCS WHERE NOTED) 58hr (UL DOCS WHERE NOTED) 59hr (UL DOCS WHERE NOTED) 60hr (UL DOCS WHERE NOTED) 61hr (UL DOCS WHERE NOTED) 62hr (UL DOCS WHERE NOTED) 63hr (UL DOCS WHERE NOTED) 64hr (UL DOCS WHERE NOTED) 65hr (UL DOCS WHERE NOTED) 66hr (UL DOCS WHERE NOTED) 67hr (UL DOCS WHERE NOTED) 68hr (UL DOCS WHERE NOTED) 69hr (UL DOCS WHERE NOTED) 70hr (UL DOCS WHERE NOTED) 71hr (UL DOCS WHERE NOTED) 72hr (UL DOCS WHERE NOTED) 73hr (UL DOCS WHERE NOTED) 74hr (UL DOCS WHERE NOTED) 75hr (UL DOCS WHERE NOTED) 76hr (UL DOCS WHERE NOTED) 77hr (UL DOCS WHERE NOTED) 78hr (UL DOCS WHERE NOTED) 79hr (UL DOCS WHERE NOTED) 80hr (UL DOCS WHERE NOTED) 81hr (UL DOCS WHERE NOTED) 82hr (UL DOCS WHERE NOTED) 83hr (UL DOCS WHERE NOTED) 84hr (UL DOCS WHERE NOTED) 85hr (UL DOCS WHERE NOTED) 86hr (UL DOCS WHERE NOTED) 87hr (UL DOCS WHERE NOTED) 88hr (UL DOCS WHERE NOTED) 89hr (UL DOCS WHERE NOTED) 90hr (UL DOCS WHERE NOTED) 91hr (UL DOCS WHERE NOTED) 92hr (UL DOCS WHERE NOTED) 93hr (UL DOCS WHERE NOTED) 94hr (UL DOCS WHERE NOTED) 95hr (UL DOCS WHERE NOTED) 96hr (UL DOCS WHERE NOTED) 97hr (UL DOCS WHERE NOTED) 98hr (UL DOCS WHERE NOTED) 99hr (UL DOCS WHERE NOTED) 100hr (UL DOCS WHERE NOTED)</p> <p>MASONRY WALL Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (UL DOCS WHERE NOTED) 17hr (UL DOCS WHERE NOTED) 18hr (UL DOCS WHERE NOTED) 19hr (UL DOCS WHERE NOTED) 20hr (UL DOCS WHERE NOTED) 21hr (UL DOCS WHERE NOTED) 22hr (UL DOCS WHERE NOTED) 23hr (UL DOCS WHERE NOTED) 24hr (UL DOCS WHERE NOTED) 25hr (UL DOCS WHERE NOTED) 26hr (UL DOCS WHERE NOTED) 27hr (UL DOCS WHERE NOTED) 28hr (UL DOCS WHERE NOTED) 29hr (UL DOCS WHERE NOTED) 30hr (UL DOCS WHERE NOTED) 31hr (UL DOCS WHERE NOTED) 32hr (UL DOCS WHERE NOTED) 33hr (UL DOCS WHERE NOTED) 34hr (UL DOCS WHERE NOTED) 35hr (UL DOCS WHERE NOTED) 36hr (UL DOCS WHERE NOTED) 37hr (UL DOCS WHERE NOTED) 38hr (UL DOCS WHERE NOTED) 39hr (UL DOCS WHERE NOTED) 40hr (UL DOCS WHERE NOTED) 41hr (UL DOCS WHERE NOTED) 42hr (UL DOCS WHERE NOTED) 43hr (UL DOCS WHERE NOTED) 44hr (UL DOCS WHERE NOTED) 45hr (UL DOCS WHERE NOTED) 46hr (UL DOCS WHERE NOTED) 47hr (UL DOCS WHERE NOTED) 48hr (UL DOCS WHERE NOTED) 49hr (UL DOCS WHERE NOTED) 50hr (UL DOCS WHERE NOTED) 51hr (UL DOCS WHERE NOTED) 52hr (UL DOCS WHERE NOTED) 53hr (UL DOCS WHERE NOTED) 54hr (UL DOCS WHERE NOTED) 55hr (UL DOCS WHERE NOTED) 56hr (UL DOCS WHERE NOTED) 57hr (UL DOCS WHERE NOTED) 58hr (UL DOCS WHERE NOTED) 59hr (UL DOCS WHERE NOTED) 60hr (UL DOCS WHERE NOTED) 61hr (UL DOCS WHERE NOTED) 62hr (UL DOCS WHERE NOTED) 63hr (UL DOCS WHERE NOTED) 64hr (UL DOCS WHERE NOTED) 65hr (UL DOCS WHERE NOTED) 66hr (UL DOCS WHERE NOTED) 67hr (UL DOCS WHERE NOTED) 68hr (UL DOCS WHERE NOTED) 69hr (UL DOCS WHERE NOTED) 70hr (UL DOCS WHERE NOTED) 71hr (UL DOCS WHERE NOTED) 72hr (UL DOCS WHERE NOTED) 73hr (UL DOCS WHERE NOTED) 74hr (UL DOCS WHERE NOTED) 75hr (UL DOCS WHERE NOTED) 76hr (UL DOCS WHERE NOTED) 77hr (UL DOCS WHERE NOTED) 78hr (UL DOCS WHERE NOTED) 79hr (UL DOCS WHERE NOTED) 80hr (UL DOCS WHERE NOTED) 81hr (UL DOCS WHERE NOTED) 82hr (UL DOCS WHERE NOTED) 83hr (UL DOCS WHERE NOTED) 84hr (UL DOCS WHERE NOTED) 85hr (UL DOCS WHERE NOTED) 86hr (UL DOCS WHERE NOTED) 87hr (UL DOCS WHERE NOTED) 88hr (UL DOCS WHERE NOTED) 89hr (UL DOCS WHERE NOTED) 90hr (UL DOCS WHERE NOTED) 91hr (UL DOCS WHERE NOTED) 92hr (UL DOCS WHERE NOTED) 93hr (UL DOCS WHERE NOTED) 94hr (UL DOCS WHERE NOTED) 95hr (UL DOCS WHERE NOTED) 96hr (UL DOCS WHERE NOTED) 97hr (UL DOCS WHERE NOTED) 98hr (UL DOCS WHERE NOTED) 99hr (UL DOCS WHERE NOTED) 100hr (UL DOCS WHERE NOTED)</p> <p>FLURRING WALL Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (UL DOCS WHERE NOTED) 17hr (UL DOCS WHERE NOTED) 18hr (UL DOCS WHERE NOTED) 19hr (UL DOCS WHERE NOTED) 20hr (UL DOCS WHERE NOTED) 21hr (UL DOCS WHERE NOTED) 22hr (UL DOCS WHERE NOTED) 23hr (UL DOCS WHERE NOTED) 24hr (UL DOCS WHERE NOTED) 25hr (UL DOCS WHERE NOTED) 26hr (UL DOCS WHERE NOTED) 27hr (UL DOCS WHERE NOTED) 28hr (UL DOCS WHERE NOTED) 29hr (UL DOCS WHERE NOTED) 30hr (UL DOCS WHERE NOTED) 31hr (UL DOCS WHERE NOTED) 32hr (UL DOCS WHERE NOTED) 33hr (UL DOCS WHERE NOTED) 34hr (UL DOCS WHERE NOTED) 35hr (UL DOCS WHERE NOTED) 36hr (UL DOCS WHERE NOTED) 37hr (UL DOCS WHERE NOTED) 38hr (UL DOCS WHERE NOTED) 39hr (UL DOCS WHERE NOTED) 40hr (UL DOCS WHERE NOTED) 41hr (UL DOCS WHERE NOTED) 42hr (UL DOCS WHERE NOTED) 43hr (UL DOCS WHERE NOTED) 44hr (UL DOCS WHERE NOTED) 45hr (UL DOCS WHERE NOTED) 46hr (UL DOCS WHERE NOTED) 47hr (UL DOCS WHERE NOTED) 48hr (UL DOCS WHERE NOTED) 49hr (UL DOCS WHERE NOTED) 50hr (UL DOCS WHERE NOTED) 51hr (UL DOCS WHERE NOTED) 52hr (UL DOCS WHERE NOTED) 53hr (UL DOCS WHERE NOTED) 54hr (UL DOCS WHERE NOTED) 55hr (UL DOCS WHERE NOTED) 56hr (UL DOCS WHERE NOTED) 57hr (UL DOCS WHERE NOTED) 58hr (UL DOCS WHERE NOTED) 59hr (UL DOCS WHERE NOTED) 60hr (UL DOCS WHERE NOTED) 61hr (UL DOCS WHERE NOTED) 62hr (UL DOCS WHERE NOTED) 63hr (UL DOCS WHERE NOTED) 64hr (UL DOCS WHERE NOTED) 65hr (UL DOCS WHERE NOTED) 66hr (UL DOCS WHERE NOTED) 67hr (UL DOCS WHERE NOTED) 68hr (UL DOCS WHERE NOTED) 69hr (UL DOCS WHERE NOTED) 70hr (UL DOCS WHERE NOTED) 71hr (UL DOCS WHERE NOTED) 72hr (UL DOCS WHERE NOTED) 73hr (UL DOCS WHERE NOTED) 74hr (UL DOCS WHERE NOTED) 75hr (UL DOCS WHERE NOTED) 76hr (UL DOCS WHERE NOTED) 77hr (UL DOCS WHERE NOTED) 78hr (UL DOCS WHERE NOTED) 79hr (UL DOCS WHERE NOTED) 80hr (UL DOCS WHERE NOTED) 81hr (UL DOCS WHERE NOTED) 82hr (UL DOCS WHERE NOTED) 83hr (UL DOCS WHERE NOTED) 84hr (UL DOCS WHERE NOTED) 85hr (UL DOCS WHERE NOTED) 86hr (UL DOCS WHERE NOTED) 87hr (UL DOCS WHERE NOTED) 88hr (UL DOCS WHERE NOTED) 89hr (UL DOCS WHERE NOTED) 90hr (UL DOCS WHERE NOTED) 91hr (UL DOCS WHERE NOTED) 92hr (UL DOCS WHERE NOTED) 93hr (UL DOCS WHERE NOTED) 94hr (UL DOCS WHERE NOTED) 95hr (UL DOCS WHERE NOTED) 96hr (UL DOCS WHERE NOTED) 97hr (UL DOCS WHERE NOTED) 98hr (UL DOCS WHERE NOTED) 99hr (UL DOCS WHERE NOTED) 100hr (UL DOCS WHERE NOTED)</p>	<p>FLURRING Type Mark: PARTITION Fire Rating Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (UL DOCS WHERE NOTED) 17hr (UL DOCS WHERE NOTED) 18hr (UL DOCS WHERE NOTED) 19hr (UL DOCS WHERE NOTED) 20hr (UL DOCS WHERE NOTED) 21hr (UL DOCS WHERE NOTED) 22hr (UL DOCS WHERE NOTED) 23hr (UL DOCS WHERE NOTED) 24hr (UL DOCS WHERE NOTED) 25hr (UL DOCS WHERE NOTED) 26hr (UL DOCS WHERE NOTED) 27hr (UL DOCS WHERE NOTED) 28hr (UL DOCS WHERE NOTED) 29hr (UL DOCS WHERE NOTED) 30hr (UL DOCS WHERE NOTED) 31hr (UL DOCS WHERE NOTED) 32hr (UL DOCS WHERE NOTED) 33hr (UL DOCS WHERE NOTED) 34hr (UL DOCS WHERE NOTED) 35hr (UL DOCS WHERE NOTED) 36hr (UL DOCS WHERE NOTED) 37hr (UL DOCS WHERE NOTED) 38hr (UL DOCS WHERE NOTED) 39hr (UL DOCS WHERE NOTED) 40hr (UL DOCS WHERE NOTED) 41hr (UL DOCS WHERE NOTED) 42hr (UL DOCS WHERE NOTED) 43hr (UL DOCS WHERE NOTED) 44hr (UL DOCS WHERE NOTED) 45hr (UL DOCS WHERE NOTED) 46hr (UL DOCS WHERE NOTED) 47hr (UL DOCS WHERE NOTED) 48hr (UL DOCS WHERE NOTED) 49hr (UL DOCS WHERE NOTED) 50hr (UL DOCS WHERE NOTED) 51hr (UL DOCS WHERE NOTED) 52hr (UL DOCS WHERE NOTED) 53hr (UL DOCS WHERE NOTED) 54hr (UL DOCS WHERE NOTED) 55hr (UL DOCS WHERE NOTED) 56hr (UL DOCS WHERE NOTED) 57hr (UL DOCS WHERE NOTED) 58hr (UL DOCS WHERE NOTED) 59hr (UL DOCS WHERE NOTED) 60hr (UL DOCS WHERE NOTED) 61hr (UL DOCS WHERE NOTED) 62hr (UL DOCS WHERE NOTED) 63hr (UL DOCS WHERE NOTED) 64hr (UL DOCS WHERE NOTED) 65hr (UL DOCS WHERE NOTED) 66hr (UL DOCS WHERE NOTED) 67hr (UL DOCS WHERE NOTED) 68hr (UL DOCS WHERE NOTED) 69hr (UL DOCS WHERE NOTED) 70hr (UL DOCS WHERE NOTED) 71hr (UL DOCS WHERE NOTED) 72hr (UL DOCS WHERE NOTED) 73hr (UL DOCS WHERE NOTED) 74hr (UL DOCS WHERE NOTED) 75hr (UL DOCS WHERE NOTED) 76hr (UL DOCS WHERE NOTED) 77hr (UL DOCS WHERE NOTED) 78hr (UL DOCS WHERE NOTED) 79hr (UL DOCS WHERE NOTED) 80hr (UL DOCS WHERE NOTED) 81hr (UL DOCS WHERE NOTED) 82hr (UL DOCS WHERE NOTED) 83hr (UL DOCS WHERE NOTED) 84hr (UL DOCS WHERE NOTED) 85hr (UL DOCS WHERE NOTED) 86hr (UL DOCS WHERE NOTED) 87hr (UL DOCS WHERE NOTED) 88hr (UL DOCS WHERE NOTED) 89hr (UL DOCS WHERE NOTED) 90hr (UL DOCS WHERE NOTED) 91hr (UL DOCS WHERE NOTED) 92hr (UL DOCS WHERE NOTED) 93hr (UL DOCS WHERE NOTED) 94hr (UL DOCS WHERE NOTED) 95hr (UL DOCS WHERE NOTED) 96hr (UL DOCS WHERE NOTED) 97hr (UL DOCS WHERE NOTED) 98hr (UL DOCS WHERE NOTED) 99hr (UL DOCS WHERE NOTED) 100hr (UL DOCS WHERE NOTED)</p> <p>EXTERIOR MASONRY WALL (LB) Fire Rating Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (UL DOCS WHERE NOTED) 17hr (UL DOCS WHERE NOTED) 18hr (UL DOCS WHERE NOTED) 19hr (UL DOCS WHERE NOTED) 20hr (UL DOCS WHERE NOTED) 21hr (UL DOCS WHERE NOTED) 22hr (UL DOCS WHERE NOTED) 23hr (UL DOCS WHERE NOTED) 24hr (UL DOCS WHERE NOTED) 25hr (UL DOCS WHERE NOTED) 26hr (UL DOCS WHERE NOTED) 27hr (UL DOCS WHERE NOTED) 28hr (UL DOCS WHERE NOTED) 29hr (UL DOCS WHERE NOTED) 30hr (UL DOCS WHERE NOTED) 31hr (UL DOCS WHERE NOTED) 32hr (UL DOCS WHERE NOTED) 33hr (UL DOCS WHERE NOTED) 34hr (UL DOCS WHERE NOTED) 35hr (UL DOCS WHERE NOTED) 36hr (UL DOCS WHERE NOTED) 37hr (UL DOCS WHERE NOTED) 38hr (UL DOCS WHERE NOTED) 39hr (UL DOCS WHERE NOTED) 40hr (UL DOCS WHERE NOTED) 41hr (UL DOCS WHERE NOTED) 42hr (UL DOCS WHERE NOTED) 43hr (UL DOCS WHERE NOTED) 44hr (UL DOCS WHERE NOTED) 45hr (UL DOCS WHERE NOTED) 46hr (UL DOCS WHERE NOTED) 47hr (UL DOCS WHERE NOTED) 48hr (UL DOCS WHERE NOTED) 49hr (UL DOCS WHERE NOTED) 50hr (UL DOCS WHERE NOTED) 51hr (UL DOCS WHERE NOTED) 52hr (UL DOCS WHERE NOTED) 53hr (UL DOCS WHERE NOTED) 54hr (UL DOCS WHERE NOTED) 55hr (UL DOCS WHERE NOTED) 56hr (UL DOCS WHERE NOTED) 57hr (UL DOCS WHERE NOTED) 58hr (UL DOCS WHERE NOTED) 59hr (UL DOCS WHERE NOTED) 60hr (UL DOCS WHERE NOTED) 61hr (UL DOCS WHERE NOTED) 62hr (UL DOCS WHERE NOTED) 63hr (UL DOCS WHERE NOTED) 64hr (UL DOCS WHERE NOTED) 65hr (UL DOCS WHERE NOTED) 66hr (UL DOCS WHERE NOTED) 67hr (UL DOCS WHERE NOTED) 68hr (UL DOCS WHERE NOTED) 69hr (UL DOCS WHERE NOTED) 70hr (UL DOCS WHERE NOTED) 71hr (UL DOCS WHERE NOTED) 72hr (UL DOCS WHERE NOTED) 73hr (UL DOCS WHERE NOTED) 74hr (UL DOCS WHERE NOTED) 75hr (UL DOCS WHERE NOTED) 76hr (UL DOCS WHERE NOTED) 77hr (UL DOCS WHERE NOTED) 78hr (UL DOCS WHERE NOTED) 79hr (UL DOCS WHERE NOTED) 80hr (UL DOCS WHERE NOTED) 81hr (UL DOCS WHERE NOTED) 82hr (UL DOCS WHERE NOTED) 83hr (UL DOCS WHERE NOTED) 84hr (UL DOCS WHERE NOTED) 85hr (UL DOCS WHERE NOTED) 86hr (UL DOCS WHERE NOTED) 87hr (UL DOCS WHERE NOTED) 88hr (UL DOCS WHERE NOTED) 89hr (UL DOCS WHERE NOTED) 90hr (UL DOCS WHERE NOTED) 91hr (UL DOCS WHERE NOTED) 92hr (UL DOCS WHERE NOTED) 93hr (UL DOCS WHERE NOTED) 94hr (UL DOCS WHERE NOTED) 95hr (UL DOCS WHERE NOTED) 96hr (UL DOCS WHERE NOTED) 97hr (UL DOCS WHERE NOTED) 98hr (UL DOCS WHERE NOTED) 99hr (UL DOCS WHERE NOTED) 100hr (UL DOCS WHERE NOTED)</p> <p>MASONRY WALL Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (UL DOCS WHERE NOTED) 17hr (UL DOCS WHERE NOTED) 18hr (UL DOCS WHERE NOTED) 19hr (UL DOCS WHERE NOTED) 20hr (UL DOCS WHERE NOTED) 21hr (UL DOCS WHERE NOTED) 22hr (UL DOCS WHERE NOTED) 23hr (UL DOCS WHERE NOTED) 24hr (UL DOCS WHERE NOTED) 25hr (UL DOCS WHERE NOTED) 26hr (UL DOCS WHERE NOTED) 27hr (UL DOCS WHERE NOTED) 28hr (UL DOCS WHERE NOTED) 29hr (UL DOCS WHERE NOTED) 30hr (UL DOCS WHERE NOTED) 31hr (UL DOCS WHERE NOTED) 32hr (UL DOCS WHERE NOTED) 33hr (UL DOCS WHERE NOTED) 34hr (UL DOCS WHERE NOTED) 35hr (UL DOCS WHERE NOTED) 36hr (UL DOCS WHERE NOTED) 37hr (UL DOCS WHERE NOTED) 38hr (UL DOCS WHERE NOTED) 39hr (UL DOCS WHERE NOTED) 40hr (UL DOCS WHERE NOTED) 41hr (UL DOCS WHERE NOTED) 42hr (UL DOCS WHERE NOTED) 43hr (UL DOCS WHERE NOTED) 44hr (UL DOCS WHERE NOTED) 45hr (UL DOCS WHERE NOTED) 46hr (UL DOCS WHERE NOTED) 47hr (UL DOCS WHERE NOTED) 48hr (UL DOCS WHERE NOTED) 49hr (UL DOCS WHERE NOTED) 50hr (UL DOCS WHERE NOTED) 51hr (UL DOCS WHERE NOTED) 52hr (UL DOCS WHERE NOTED) 53hr (UL DOCS WHERE NOTED) 54hr (UL DOCS WHERE NOTED) 55hr (UL DOCS WHERE NOTED) 56hr (UL DOCS WHERE NOTED) 57hr (UL DOCS WHERE NOTED) 58hr (UL DOCS WHERE NOTED) 59hr (UL DOCS WHERE NOTED) 60hr (UL DOCS WHERE NOTED) 61hr (UL DOCS WHERE NOTED) 62hr (UL DOCS WHERE NOTED) 63hr (UL DOCS WHERE NOTED) 64hr (UL DOCS WHERE NOTED) 65hr (UL DOCS WHERE NOTED) 66hr (UL DOCS WHERE NOTED) 67hr (UL DOCS WHERE NOTED) 68hr (UL DOCS WHERE NOTED) 69hr (UL DOCS WHERE NOTED) 70hr (UL DOCS WHERE NOTED) 71hr (UL DOCS WHERE NOTED) 72hr (UL DOCS WHERE NOTED) 73hr (UL DOCS WHERE NOTED) 74hr (UL DOCS WHERE NOTED) 75hr (UL DOCS WHERE NOTED) 76hr (UL DOCS WHERE NOTED) 77hr (UL DOCS WHERE NOTED) 78hr (UL DOCS WHERE NOTED) 79hr (UL DOCS WHERE NOTED) 80hr (UL DOCS WHERE NOTED) 81hr (UL DOCS WHERE NOTED) 82hr (UL DOCS WHERE NOTED) 83hr (UL DOCS WHERE NOTED) 84hr (UL DOCS WHERE NOTED) 85hr (UL DOCS WHERE NOTED) 86hr (UL DOCS WHERE NOTED) 87hr (UL DOCS WHERE NOTED) 88hr (UL DOCS WHERE NOTED) 89hr (UL DOCS WHERE NOTED) 90hr (UL DOCS WHERE NOTED) 91hr (UL DOCS WHERE NOTED) 92hr (UL DOCS WHERE NOTED) 93hr (UL DOCS WHERE NOTED) 94hr (UL DOCS WHERE NOTED) 95hr (UL DOCS WHERE NOTED) 96hr (UL DOCS WHERE NOTED) 97hr (UL DOCS WHERE NOTED) 98hr (UL DOCS WHERE NOTED) 99hr (UL DOCS WHERE NOTED) 100hr (UL DOCS WHERE NOTED)</p> <p>FLURRING WALL Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (UL DOCS WHERE NOTED) 17hr (UL DOCS WHERE NOTED) 18hr (UL DOCS WHERE NOTED) 19hr (UL DOCS WHERE NOTED) 20hr (UL DOCS WHERE NOTED) 21hr (UL DOCS WHERE NOTED) 22hr (UL DOCS WHERE NOTED) 23hr (UL DOCS WHERE NOTED) 24hr (UL DOCS WHERE NOTED) 25hr (UL DOCS WHERE NOTED) 26hr (UL DOCS WHERE NOTED) 27hr (UL DOCS WHERE NOTED) 28hr (UL DOCS WHERE NOTED) 29hr (UL DOCS WHERE NOTED) 30hr (UL DOCS WHERE NOTED) 31hr (UL DOCS WHERE NOTED) 32hr (UL DOCS WHERE NOTED) 33hr (UL DOCS WHERE NOTED) 34hr (UL DOCS WHERE NOTED) 35hr (UL DOCS WHERE NOTED) 36hr (UL DOCS WHERE NOTED) 37hr (UL DOCS WHERE NOTED) 38hr (UL DOCS WHERE NOTED) 39hr (UL DOCS WHERE NOTED) 40hr (UL DOCS WHERE NOTED) 41hr (UL DOCS WHERE NOTED) 42hr (UL DOCS WHERE NOTED) 43hr (UL DOCS WHERE NOTED) 44hr (UL DOCS WHERE NOTED) 45hr (UL DOCS WHERE NOTED) 46hr (UL DOCS WHERE NOTED) 47hr (UL DOCS WHERE NOTED) 48hr (UL DOCS WHERE NOTED) 49hr (UL DOCS WHERE NOTED) 50hr (UL DOCS WHERE NOTED) 51hr (UL DOCS WHERE NOTED) 52hr (UL DOCS WHERE NOTED) 53hr (UL DOCS WHERE NOTED) 54hr (UL DOCS WHERE NOTED) 55hr (UL DOCS WHERE NOTED) 56hr (UL DOCS WHERE NOTED) 57hr (UL DOCS WHERE NOTED) 58hr (UL DOCS WHERE NOTED) 59hr (UL DOCS WHERE NOTED) 60hr (UL DOCS WHERE NOTED) 61hr (UL DOCS WHERE NOTED) 62hr (UL DOCS WHERE NOTED) 63hr (UL DOCS WHERE NOTED) 64hr (UL DOCS WHERE NOTED) 65hr (UL DOCS WHERE NOTED) 66hr (UL DOCS WHERE NOTED) 67hr (UL DOCS WHERE NOTED) 68hr (UL DOCS WHERE NOTED) 69hr (UL DOCS WHERE NOTED) 70hr (UL DOCS WHERE NOTED) 71hr (UL DOCS WHERE NOTED) 72hr (UL DOCS WHERE NOTED) 73hr (UL DOCS WHERE NOTED) 74hr (UL DOCS WHERE NOTED) 75hr (UL DOCS WHERE NOTED) 76hr (UL DOCS WHERE NOTED) 77hr (UL DOCS WHERE NOTED) 78hr (UL DOCS WHERE NOTED) 79hr (UL DOCS WHERE NOTED) 80hr (UL DOCS WHERE NOTED) 81hr (UL DOCS WHERE NOTED) 82hr (UL DOCS WHERE NOTED) 83hr (UL DOCS WHERE NOTED) 84hr (UL DOCS WHERE NOTED) 85hr (UL DOCS WHERE NOTED) 86hr (UL DOCS WHERE NOTED) 87hr (UL DOCS WHERE NOTED) 88hr (UL DOCS WHERE NOTED) 89hr (UL DOCS WHERE NOTED) 90hr (UL DOCS WHERE NOTED) 91hr (UL DOCS WHERE NOTED) 92hr (UL DOCS WHERE NOTED) 93hr (UL DOCS WHERE NOTED) 94hr (UL DOCS WHERE NOTED) 95hr (UL DOCS WHERE NOTED) 96hr (UL DOCS WHERE NOTED) 97hr (UL DOCS WHERE NOTED) 98hr (UL DOCS WHERE NOTED) 99hr (UL DOCS WHERE NOTED) 100hr (UL DOCS WHERE NOTED)</p>	<p>FLURRING Type Mark: PARTITION Fire Rating Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (UL DOCS WHERE NOTED) 17hr (UL DOCS WHERE NOTED) 18hr (UL DOCS WHERE NOTED) 19hr (UL DOCS WHERE NOTED) 20hr (UL DOCS WHERE NOTED) 21hr (UL DOCS WHERE NOTED) 22hr (UL DOCS WHERE NOTED) 23hr (UL DOCS WHERE NOTED) 24hr (UL DOCS WHERE NOTED) 25hr (UL DOCS WHERE NOTED) 26hr (UL DOCS WHERE NOTED) 27hr (UL DOCS WHERE NOTED) 28hr (UL DOCS WHERE NOTED) 29hr (UL DOCS WHERE NOTED) 30hr (UL DOCS WHERE NOTED) 31hr (UL DOCS WHERE NOTED) 32hr (UL DOCS WHERE NOTED) 33hr (UL DOCS WHERE NOTED) 34hr (UL DOCS WHERE NOTED) 35hr (UL DOCS WHERE NOTED) 36hr (UL DOCS WHERE NOTED) 37hr (UL DOCS WHERE NOTED) 38hr (UL DOCS WHERE NOTED) 39hr (UL DOCS WHERE NOTED) 40hr (UL DOCS WHERE NOTED) 41hr (UL DOCS WHERE NOTED) 42hr (UL DOCS WHERE NOTED) 43hr (UL DOCS WHERE NOTED) 44hr (UL DOCS WHERE NOTED) 45hr (UL DOCS WHERE NOTED) 46hr (UL DOCS WHERE NOTED) 47hr (UL DOCS WHERE NOTED) 48hr (UL DOCS WHERE NOTED) 49hr (UL DOCS WHERE NOTED) 50hr (UL DOCS WHERE NOTED) 51hr (UL DOCS WHERE NOTED) 52hr (UL DOCS WHERE NOTED) 53hr (UL DOCS WHERE NOTED) 54hr (UL DOCS WHERE NOTED) 55hr (UL DOCS WHERE NOTED) 56hr (UL DOCS WHERE NOTED) 57hr (UL DOCS WHERE NOTED) 58hr (UL DOCS WHERE NOTED) 59hr (UL DOCS WHERE NOTED) 60hr (UL DOCS WHERE NOTED) 61hr (UL DOCS WHERE NOTED) 62hr (UL DOCS WHERE NOTED) 63hr (UL DOCS WHERE NOTED) 64hr (UL DOCS WHERE NOTED) 65hr (UL DOCS WHERE NOTED) 66hr (UL DOCS WHERE NOTED) 67hr (UL DOCS WHERE NOTED) 68hr (UL DOCS WHERE NOTED) 69hr (UL DOCS WHERE NOTED) 70hr (UL DOCS WHERE NOTED) 71hr (UL DOCS WHERE NOTED) 72hr (UL DOCS WHERE NOTED) 73hr (UL DOCS WHERE NOTED) 74hr (UL DOCS WHERE NOTED) 75hr (UL DOCS WHERE NOTED) 76hr (UL DOCS WHERE NOTED) 77hr (UL DOCS WHERE NOTED) 78hr (UL DOCS WHERE NOTED) 79hr (UL DOCS WHERE NOTED) 80hr (UL DOCS WHERE NOTED) 81hr (UL DOCS WHERE NOTED) 82hr (UL DOCS WHERE NOTED) 83hr (UL DOCS WHERE NOTED) 84hr (UL DOCS WHERE NOTED) 85hr (UL DOCS WHERE NOTED) 86hr (UL DOCS WHERE NOTED) 87hr (UL DOCS WHERE NOTED) 88hr (UL DOCS WHERE NOTED) 89hr (UL DOCS WHERE NOTED) 90hr (UL DOCS WHERE NOTED) 91hr (UL DOCS WHERE NOTED) 92hr (UL DOCS WHERE NOTED) 93hr (UL DOCS WHERE NOTED) 94hr (UL DOCS WHERE NOTED) 95hr (UL DOCS WHERE NOTED) 96hr (UL DOCS WHERE NOTED) 97hr (UL DOCS WHERE NOTED) 98hr (UL DOCS WHERE NOTED) 99hr (UL DOCS WHERE NOTED) 100hr (UL DOCS WHERE NOTED)</p> <p>EXTERIOR MASONRY WALL (LB) Fire Rating Type Mark: 1hr (UL DOCS WHERE NOTED) 2hr (UL DOCS WHERE NOTED) 3hr (UL DOCS WHERE NOTED) 4hr (UL DOCS WHERE NOTED) 5hr (UL DOCS WHERE NOTED) 6hr (UL DOCS WHERE NOTED) 7hr (UL DOCS WHERE NOTED) 8hr (UL DOCS WHERE NOTED) 9hr (UL DOCS WHERE NOTED) 10hr (UL DOCS WHERE NOTED) 11hr (UL DOCS WHERE NOTED) 12hr (UL DOCS WHERE NOTED) 13hr (UL DOCS WHERE NOTED) 14hr (UL DOCS WHERE NOTED) 15hr (UL DOCS WHERE NOTED) 16hr (</p>	



Prime Contract Potential Change Order
#013: CE #016 - Fur-Out Wall at North Hallway

Created on: 5/28 /2021
Project Name: South Fire District Renovations and Addition
Project Number: 538

TO:

City of Middletown
245 Dekoven Drive
Middletown Connecticut, 06457

PROJECT:

South Fire District Renovations and Addition
445 Randolph Road
Middletown, Connecticut 06457

REQUEST RECEIVED FROM:

LOCATION:

FROM:

Enterprise Builders, Inc.
46 Shepard Drive
Newington Connecticut, 06111

CONTRACT:

1 - South Fire District Prime Contract

STATUS:

Draft

ACCOUNTING METHOD:

Amount Based

TOTAL AMOUNT:

\$2,990.00

POTENTIAL CHANGE ORDER TITLE: CE #016 - Fur-Out Wall at North Hallway

CHANGE REASON: Owner

POTENTIAL CHANGE ORDER DESCRIPTION: *(The Contract Is Changed As Follows)*

CE #016 - Fur-Out Wall at North Hallway
Owner wants to fur-out Wall at North Hallway"

REFERENCES / ATTACHMENTS:

[MCM Acoustics Quote.pdf](#) [Superior Painting Quote.pdf](#) [plan wiht note.pdf](#)

SCHEDULE IMPACT: 0 days

#	SubJob	Cost Code	Description	Type	Amount
1	N/A	9-09-250 - Gypsum Board	MCM: Fur Out Wall with 1 5/8" Channel and 5/8" Drywall per quote dated 5/18/21	Subcontract	\$ 2,448.00
2	N/A	9-09-900 - Painting	Superior Painting: Prime and Paint addition Wall in Corridor Approx 200 sqft per Superior Change Order Proposal	Subcontract	\$ 400.00
Subtotal:					\$2,848.00
	20-001-0 EBI: 5% OH&P (1/01-175-O): ≈ 4.99% Applies to Materials, Commitment, Allowances, Subcontract, and Labor.				\$ 142.00
Grand Total:					\$2,990.00



Enterprise Builders, Inc.

A handwritten signature in blue ink, consisting of a large, stylized 'E' followed by a horizontal line.

By

6/7/21

Date

Approved on behalf of City of Middletown

By

Date

Affirmative Action / Equal Opportunity Employer



Proposal

Date

5/18/2021

Furred out wall @ north hallway
South fire district

Submitted to Enterprise builders
Christian/Kyle

We propose to provide :

☐

Labor and material

☒

Furr out wall @ north Hallway
1 5/8" channel with 5/8 sheetrock

L \$2,148
M \$300

Total

\$2,448.00

Notes:

*No dumpster fees included
Tax exempt*

Sincerely,
Isaac Williams

Superior Painting LLC

66 Borghesi CT
Wolcott, CT 06716
P 203-441-4089 F 203 441-4124
HIC# 0624098
superiorpaintingllc@comcast.net
DAS SBE certified

CHANGE ORDER PROPOSAL

Date:

To: Estimating

Attn:

Fax:

From: Robert Sanseverino

We are pleased to submit our proposal for 09910 Painting

PROJECT: South Fire

Base Price: 400.00

Scope:

Prime and Paint addition Wall in Corridor Approx 200 sqft.

Open Shop

Superior Finishes at Affordable pricing

lockers (36) to be
ted at the end of
I, Coordinate with
ation's Personnel

ows & Reuse is
Phase I, Provide
ure to Protect
aces to Remain

Remove at the
nd of Phase II


ld Temporary
n at Phase I,
n at Phase III

ns at Phase
a to be Built
at Phase III

Area to be
s a Hallway
ing Phase II

Reuse as
ide Temp.
Existing
o Remain

Addition Renovation

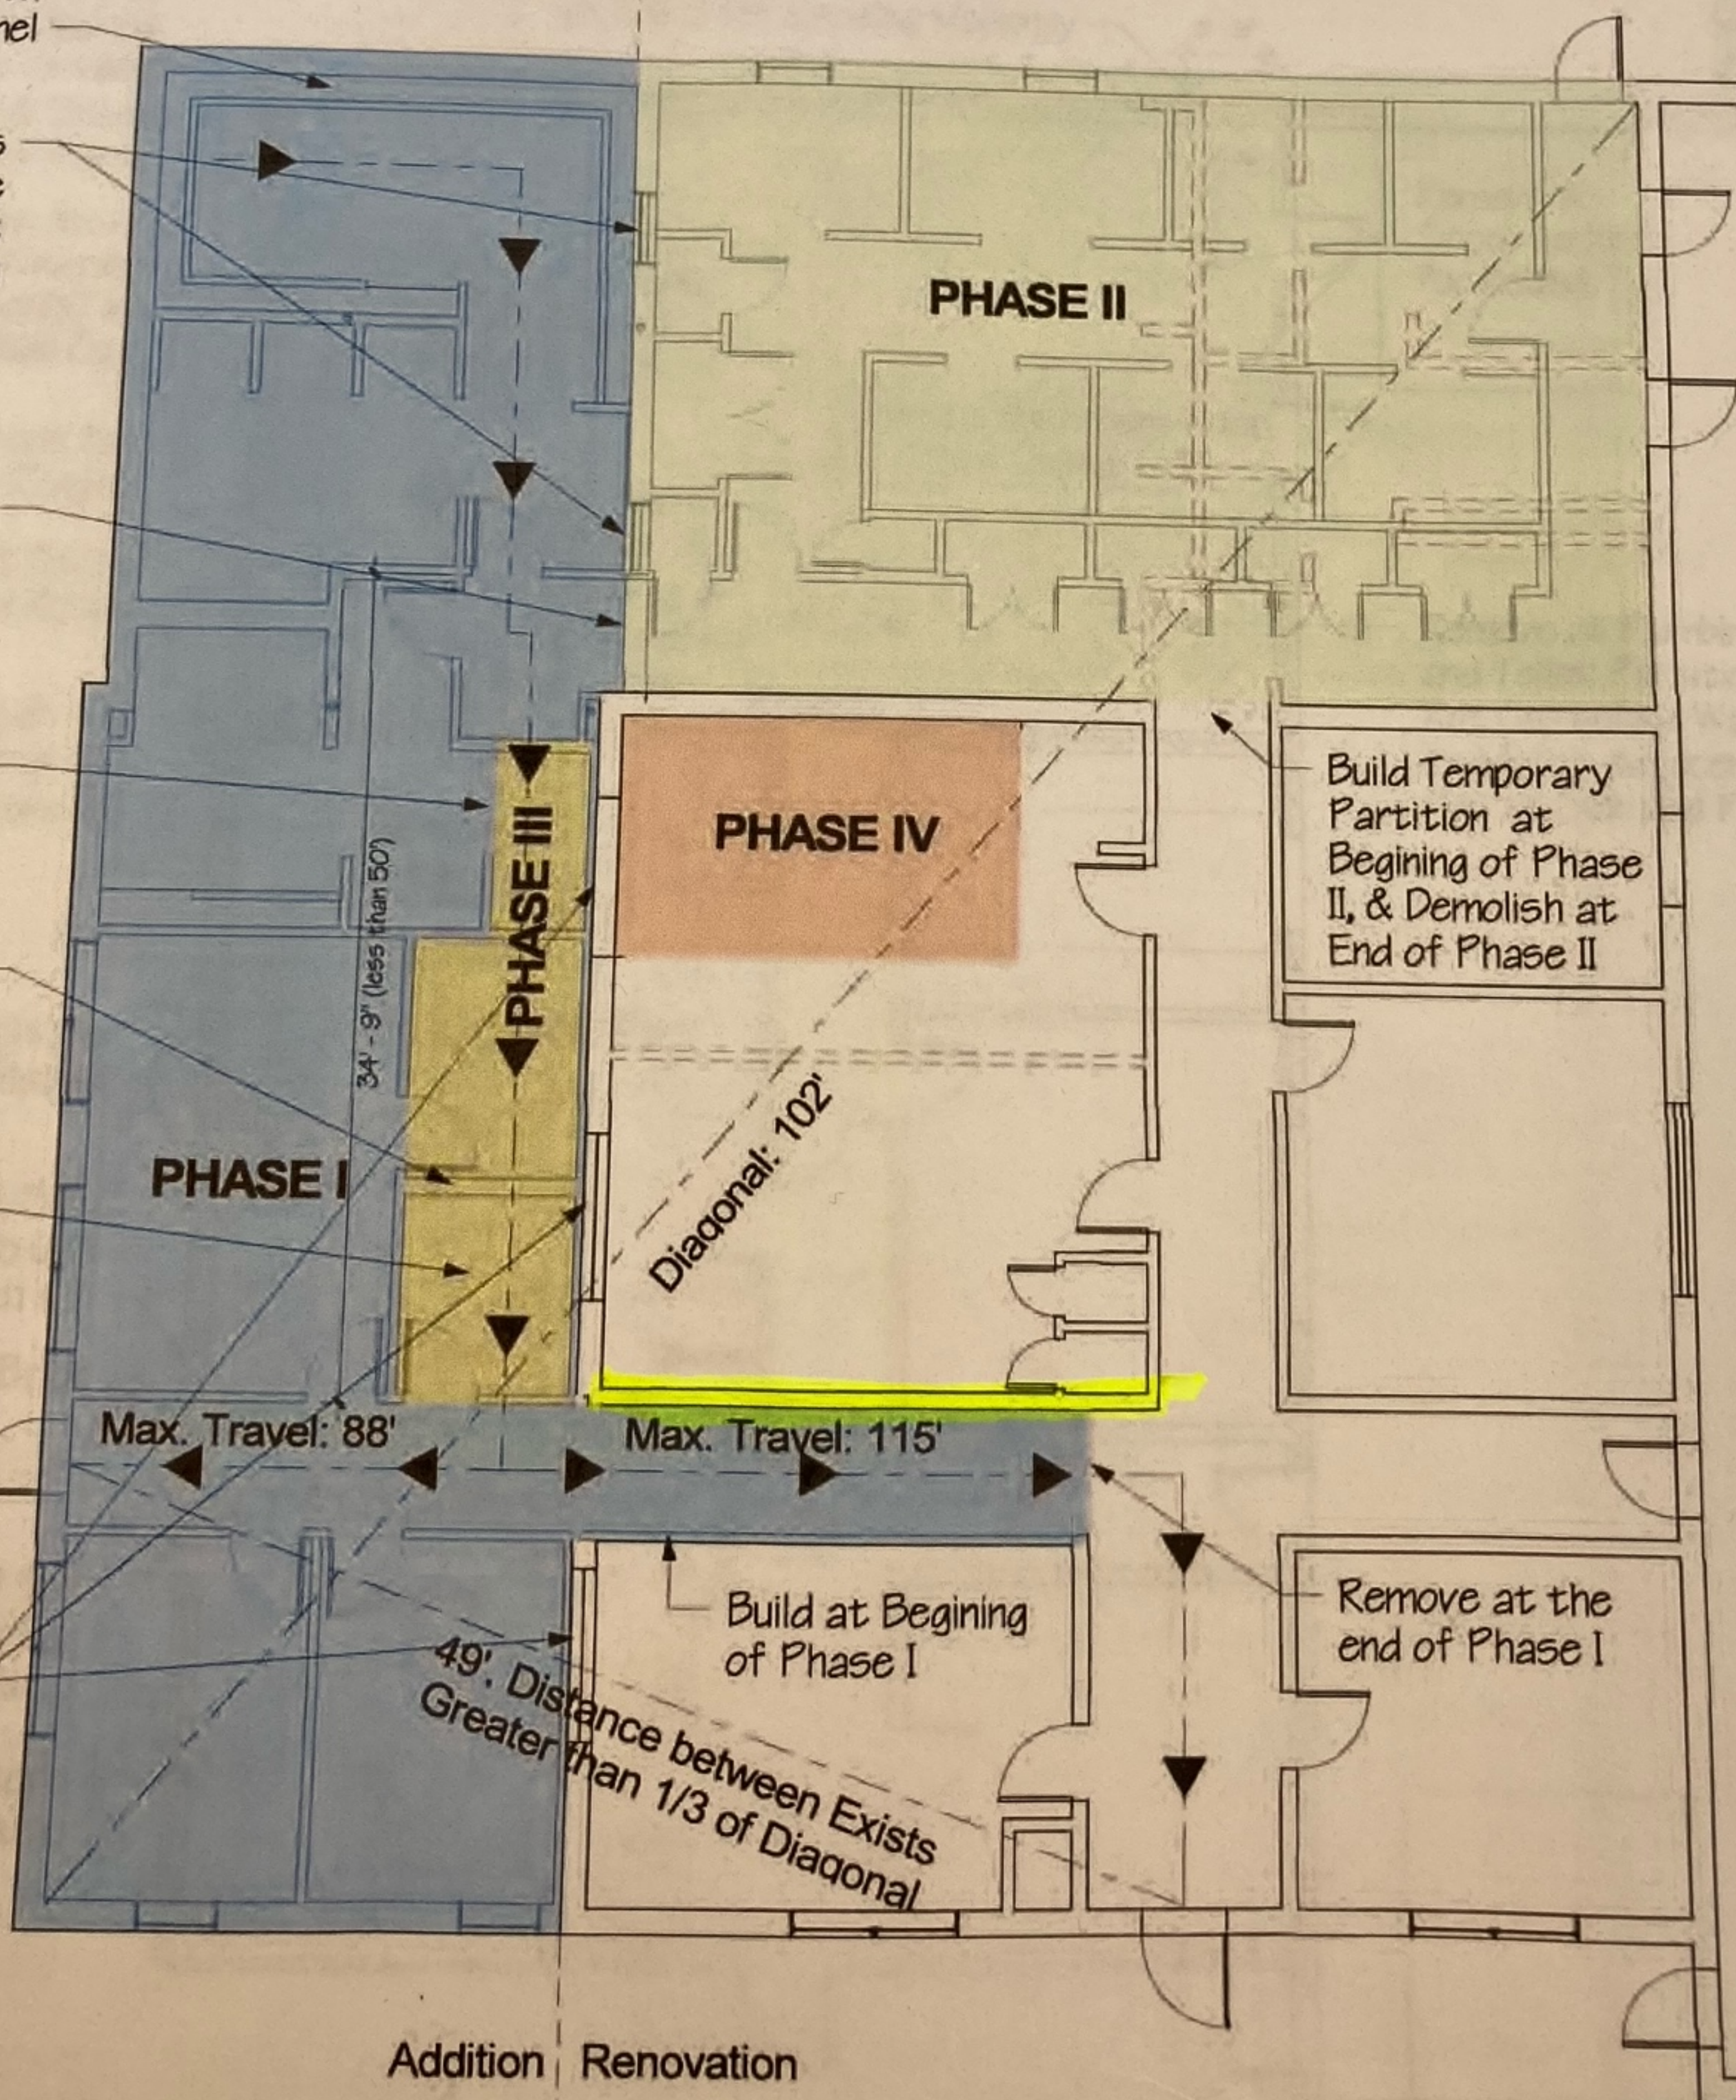

Build Temporary
Partition at
Beginning of Phase
II, & Demolish at
End of Phase II

Remove at the
end of Phase I

Addition Renovation



Prime Contract Potential Change Order

**#014-R1: CE #017 - Additional Five (5) NOT
WELDED Lockers**

Created on: 5/28 /2021
Project Name: South Fire District Renovations and Addition
Project Number: 538

TO:

City of Middletown
245 Dekoven Drive
Middletown Connecticut, 06457

PROJECT:

South Fire District Renovations and Addition
445 Randolph Road
Middletown, Connecticut 06457

REQUEST RECEIVED FROM:

LOCATION:

FROM:

Enterprise Builders, Inc.
46 Shepard Drive
Newington Connecticut, 06111

CONTRACT:

1 - South Fire District Prime Contract

STATUS:

Draft

ACCOUNTING METHOD:

Amount Based

TOTAL AMOUNT:

\$2,035.00

POTENTIAL CHANGE ORDER TITLE: CE #017 - Additional Five (5) NOT WELDED Lockers

CHANGE REASON: Field Conditions

POTENTIAL CHANGE ORDER DESCRIPTION: *(The Contract Is Changed As Follows)*

CE #017 - Additional Five (5) NOT WELDED Lockers

Existing Lockers to be Re-Used are too deep therefore, Owner requested five (5) new lockers to go into the new opening

Due to long lead time (16 to 18 weeks), EBI recommends NOT WELDED Lockers (4 to 6 weeks)

REFERENCES / ATTACHMENTS:

[FORD & ULRICH QUOTE.pdf](#) [ASI Traditional Locker Cut sheet.pdf](#)

SCHEDULE IMPACT: 0 days

#	SubJob	Cost Code	Description	Type	Amount
1	N/A	10-10-500 - Lockers	Ford & Ulrich: Additional Five (5) Lockers – NOT WELDED (per quote dated 5/27/21)	Subcontract	\$ 1,938.00
Subtotal:					\$1,938.00
	20-001-0 EBI: 5% OH&P (1/01-175-O): ≈ 5.01% Applies to Materials, Commitment, Allowances, Subcontract, and Labor.				\$ 97.00
Grand Total:					\$2,035.00



Enterprise Builders, Inc.

By

Date

Approved on behalf of City of Middletown

By

Date

Affirmative Action / Equal Opportunity Employer



459 WASHINGTON AVE
P.O. BOX 213
NORTH HAVEN, CT 06473
203-239-4451 PHONE

May 27, 2021
QUOTE #111-R2

ENTERPRISE BUILDERS
46 SHEPARD DRIVE
NEWINGTON, CT 06111
ATTN: CHRISTIAN MAZZETTI
PHONE: 860-212-5684
cmazzetti@enterbuilders.com

REF: SOUTH FIRE DISTRICT - MIDDLETOWN CT

We are pleased to offer the following quote		Price	UOM	Extended
[1]	ASI TRADITIONAL LOCKERS	\$1,938.00	LOT	\$1,938.00

[5] 1-Tier Traditional Lockers
15"W x 18"D x 72"H
No Legs – No Base - Flat Top

Notes:

Quoted per Elevations and Customer Quantities
Locks by others
Includes Louver Ventilation
Includes Multipoint Latching
Lockers Delivered Assembled to Site
Customer to Receive and Install
Lockers to be Mounted Flush to Wall
Blocking in Walls by others
Color from ASI's Standard Color Chart - Powder Coated Finish

Based on my interpretation of plans & specs
Pricing Based on 2021 Delivery and Installation
Pricing does not include taxes
Requires use of Elevator @ N/C for Upper Levels

This quotation is valid for 30 days

Terms: TO BE ARRANGED

Delivery: Welded Lockers: 16-18 Weeks ARO and Approved Submittals

Riveted Lockers: 4-6 Weeks ARO and Approved Submittals

FOB: Delivered

Michael Tringali
Michael Tringali

"To ensure accuracy, it is your responsibility to review this quote and contact us with any discrepancies, updates or questions. We will be happy to consult with you on any changes."



459 WASHINGTON AVE
P.O. BOX 213
NORTH HAVEN, CT 06473
203-239-4451 PHONE

State of CT Minority Business Enterprise Initiative

Ford & Ulrich is now a Woman Owned - Small / Minority Business Enterprise certified with the State of Connecticut. This may help with your Supplier Diversity Initiative on this project. Our Certificate is available upon request to include in your files for your Supplier Diversity program. For a list of program approved Goods & Services go to <http://www.biznet.ct.gov/SDCert?CID=553>

State of Connecticut

Department of Administrative Services
Supplier Diversity Program

This Certifies

Ford & Ulrich, Inc.

459 Washington Avenue North Haven CT 06473

Woman Owned

As a

Small/Minority Business Enterprise

February 28, 2020 through February 28, 2022

Owner(s): Ewa Penisse; V.J. Penisse

Contact: Ewa Penisse

Telephone: (203) 239-4451 Ext:

FAX: (203) 239-4454

E-Mail: ewa@fordulrich.com

Web Address: www.fordulrich.com

****Affiliate Companies:** EDS Assembly, LLC


Supplier Diversity Director

Supplier Diversity Specialist

** A contractor awarded a contract or a portion of a contract under the set-aside program shall not subcontract with any person(s) with whom the contractor is affiliated.

SINGLE TIER LOCKER

Date Issued 01-17

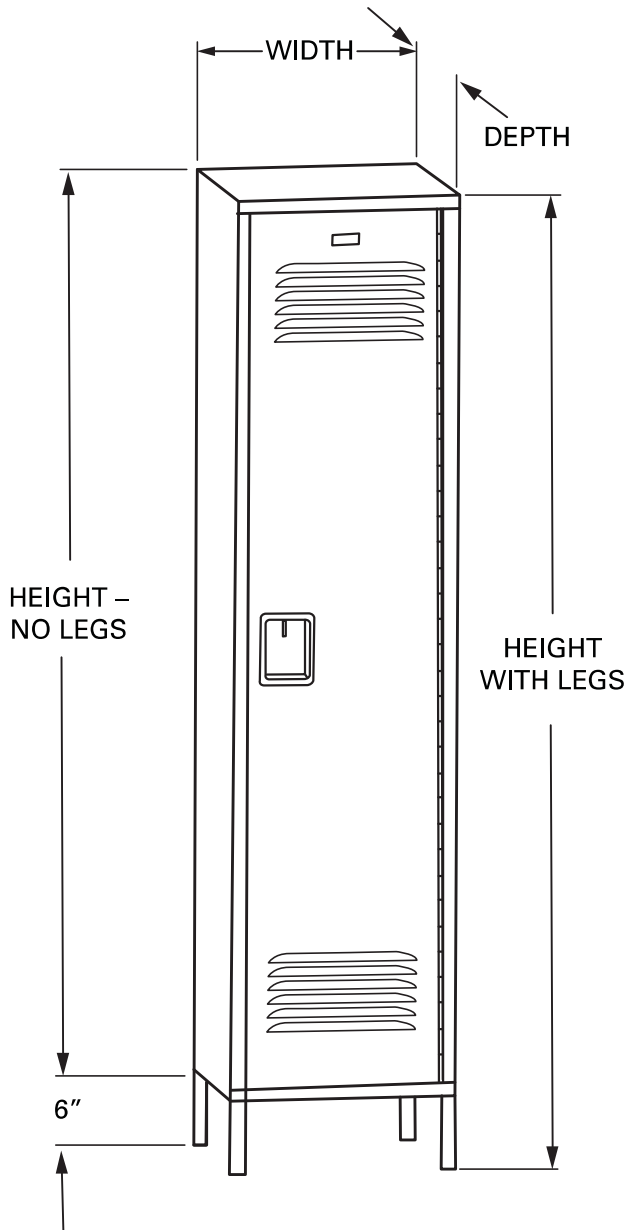

		HEIGHT WITH LEGS			
WIDTH	DEPTH	42	54	66	78
12	12				
12	15				
12	18				
15	15	N/A	N/A		
15	18	N/A	N/A		
18	18	N/A	N/A		

		HEIGHT - NO LEGS			
WIDTH	DEPTH	36	48	60	72
12	12				
12	15				
12	18				
15	15	N/A	N/A		
15	18	N/A	N/A		
18	18	N/A	N/A		

THIS MANUFACTURER RESERVES THE RIGHT TO MAKE CHANGES IN DESIGN OR DIMENSIONS WITHOUT FORMAL NOTICE

SPECIFICATION

Material – All major steel parts shall be of mild cold rolled commercial quality steel.

Finish – All material shall be power washed and phosphate treated for maximum finish color adhesion. All components shall be finished with a hybrid epoxy/polyester powder, electrostatically applied to ensure uniform thickness and baked to cure.

Construction – All lockers shall be built on a unit principle with common intermediate uprights separating units.

Door Frames – Shall be 16 gauge formed in a channel shape. Vertical members shall have additional flange to provide a continuous door strike. Cross frame members shall also be 16 gauge channel shaped.

Doors – Shall be 16 gauge with louvers for ventilation, channel shaped on both the lock and hinge side, with angle formations across the top and bottom.

Body – Bottoms shall be 16 gauge. Tops, sides, backs and shelves shall be 24 gauge. Bolt spacing shall not exceed 9" o.c.

Hinges – Shall be full length 16 gauge continuous piano type riveted to both door and frame.

Handles – Shall be one-piece 20 gauge deep drawn stainless steel cup designed to accommodate locks.

Latching – The lifting trigger shall be 14 gauge steel, attached to the latching channel. The trigger shall have a padlock eye for use with 9/32" diameter padlock shackle. Doors to have latch clip engaging frame at three points on doors over 42" high and two points on all other doors. Locking device to be positive automatic type, whereby locker door may be locked when open, then closed without unlocking. A rubber silencer shall be firmly secured to the frame at each latch hook.

Interior Equipment – Lockers 48" or higher shall be equipped with a shelf. If under 18" deep, locker shall have three wall hooks and one ceiling hook. Lockers 18" deep or more shall have a coat rod instead of a ceiling hook. Lockers 15" and 18" wide shall have four wall hooks and one ceiling hook.

Number Plates – Each locker shall have a polished aluminum number plate riveted to door frame with black numerals 3/8" high.

Color – Doors and exposed body parts shall be selected from ASI Storage Solution's standard design color range. Non-exposed body parts shall be finished in #03 Almond or #25 Gray with #25 Gray exterior.

Assembly – Factory assembled lockers shall be riveted. Knocked Down "KD" lockers shall be supplied with nuts and bolts unless otherwise specified.

Installation – Lockers shall be installed in accordance with ASI Storage Solution's installation instructions and shall be level and plumb with flush surfaces and rigid attachment to anchoring surfaces.
